Portfolio Report

- Capex LB
- Opex Development

Mar- 2026

Contenido

1. Portafolio Capex
   - Capex por Areas
   - Forecast Abr-2026 por Areas y Responsables / Capex
2. Portafolio Opex Development & Resource Development
   - Opex por Areas
   - Forecast Abr-2026 por Areas y Responsables / Opex

LB Capex

Capex Portfolio Status

CAPEX Report 2026 (As of Mar-26)

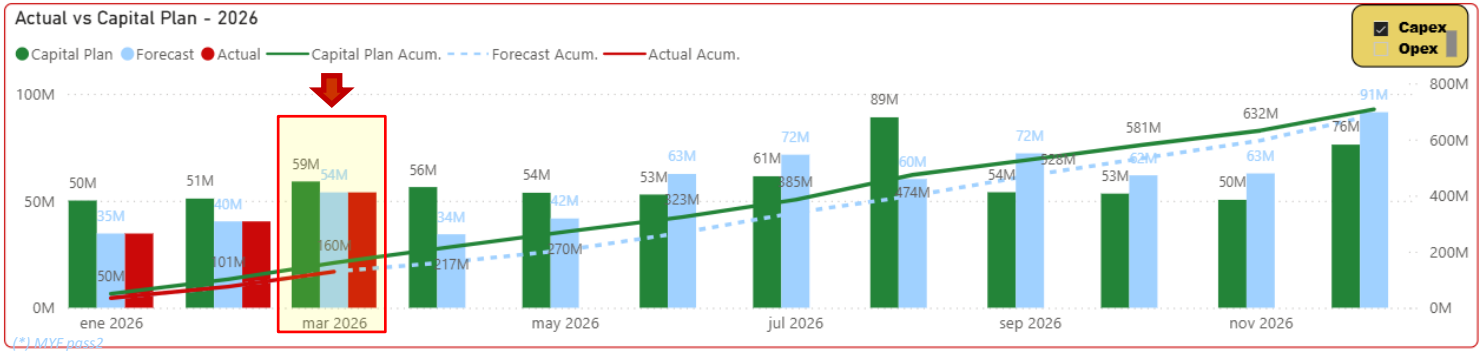

707.8M	Capital Plan
687.6M	Forecast
160.2M	YTD (CP)
129.0M	Actual to date
394.1M	Open Commit

Summary by Areas (YTD)



Summary by Areas with Year To Go 2026

N°	Grupo	Capital Plan	Forecast	Actual	YTG (CP)	O. Comm.	New Comm.
5	Land	53.92M	52.23M	1.03M	52.89M	2.41M	50.48M
4	Resource Development	16.56M	17.42M	1.31M	15.26M	2.56M	12.69M
3	Others	184.01M	157.99M	25.44M	158.57M	79.76M	78.81M
2	Implementation	414.81M	427.84M	93.98M	310.03M	303.98M	6.04M
1	Studies	38.45M	31.88M	7.20M	31.25M	5.41M	25.85M
Total		**707.75M**	**687.56M**	**128.99M**	**578.76M**	**394.13M**	**184.63M**

Status for Mar-26

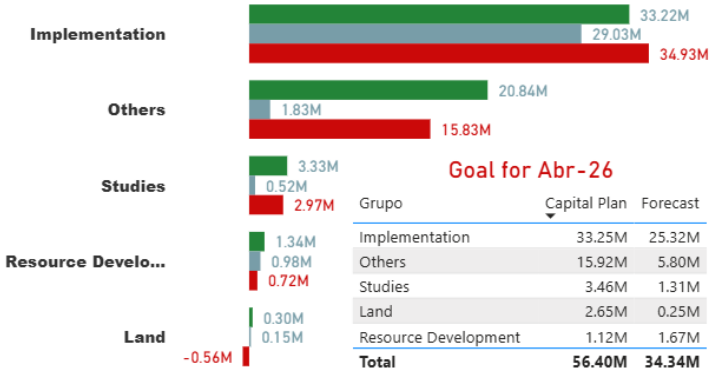

Goal for Abr-26

Grupo	Capital Plan	Forecast
Implementation	33.25M	25.32M
Others	15.92M	5.80M
Studies	3.46M	1.31M
Land	2.65M	0.25M
Resource Development	1.12M	1.67M
Total	**56.40M**	**34.34M**

* Previous forecast

Capex Portfolio Status / Desviations by Area / Mar-26 Results

Capital completion rate :

- ≥ 80%
- 75% ≤ r < 80%
- < 75%

Group	Executed by	Budget	Actual Mar-26	Budget Mar-26	Var Mar-26	Actual YTD	Budget YTD	Var YTD	Budget Abr-26	Fcast Abr-26	Var Abr-26 Fcast vs Budget
Project Delivery	DevelopStudies	38.5	3.0	3.3	-0.4	7.2	10.2	-3.0	3.5	1.3	-2.2
	ProjectDelivery	414.8	34.9	33.2	1.7	94.0	102.0	-8.0	33.2	25.3	-7.9
Resource Development	ResourceDevelopm	16.6	0.7	1.3	-0.6	1.3	4.4	-3.1	1.1	1.7	0.5
Land Access	LandAccess	53.9	-0.6	0.3	-0.9	1.0	0.3	0.7	2.7	0.2	-2.4
Mine Operation & Others	Maintenance	97.0	14.0	17.7	-3.7	19.9	35.3	-15.3	11.7	3.6	-8.2
	MineOper	45.0	0.1	0.6	-0.5	2.6	1.1	1.5	0.2	0.0	-0.2
	TechServices	19.1	1.2	1.8	-0.6	2.1	4.7	-2.6	1.5	1.0	-0.5
	Logistics	1.3	0.0	0.1	-0.1	0.0	0.2	-0.2	0.1	0.0	-0.1
	IT-TechServ	13.6	0.0	0.5	-0.5	0.0	0.8	-0.8	1.6	0.0	-1.6
	ConcentPlant	1.6	0.4	0.0	0.4	0.4	0.2	0.2	0.0	0.6	0.6
	StrategPlan	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	SHE	0.1	0.0	0.1	-0.1	0.0	0.1	0.0	0.0	0.0	0.0
	Water&Tailings	1.7	0.2	0.1	0.1	0.4	0.5	-0.1	0.2	0.7	0.4
	CCRR	3.6	0.0	0.0	0.0	0.0	0.0	0.0	0.2	0.0	-0.2
	Others	0.9	0.0	0.0	0.0	0.0	0.3	-0.3	0.4	0.0	-0.4
	Total US$M	**707.8**	**53.9**	**59.0**	**-5.1**	**129.0**	**160.2**	**-31.2**	**56.4**	**34.3**	**-22.1**

Capex Portfolio Status / Main desviations / Mar-26 Results

		Month			YTD						Factors under control				Uncertainty Factors		
Executed by	**Project**	Actual	Bud	Var	Actual	Bud	Var	**Reason**	**Action**	Criticality	APF approval	Supply / Bidding process	Projects in Execution / Re scheduling	Projects under definition	Permits and access	Contracts with Communities	Land / CCRR / Negotiation process
ProjectDelivery	Chalcobamba 1 Ph2 (Sustaining)	6.06	3.38	2.68	14.36	9.98	4.39	Execution of additional activities	-	Non-critical			4.39				
ProjectDelivery	Pit FB Phase 6 - Infrastructure (IMP)	7.89	4.10	3.78	20.56	14.19	6.37	Greater progress in electrical works, T6 Channel, Truck Shop, and Geology	-	Non-critical			6.37				
ProjectDelivery	TD&RWI Pumping System (5&6)_Phase2 (IMP)	7.11	4.37	2.74	19.54	12.81	6.73	Higher costs incurred due to partial provisioning of overhead expenses currently under review and closure	-	Non-critical			6.73				
ProjectDelivery	Pit FB Phase 6B - Infrastructure (IMP)	2.00	2.30	(0.30)	9.93	6.49	3.43	Early earthworks at Ticona access.	-	Non-critical			3.43				
ProjectDelivery	Foaming excess control in flotation	0.07	0.50	(0.43)	0.21	2.49	(2.28)	Delay in engineering development and award.	Ensure that the prior engineering phase is completed.	Non-critical				(2.28)			
ProjectDelivery	Pionero Waste Dump (IMP)	0.67	3.21	(2.54)	0.78	9.62	(8.84)	Delay in the start of works due to late contract award and area interferences affecting the commencement of main packages	Prioritize finalizing the awarding processes	Critical		(8.84)					
ProjectDelivery	DMO Ferro 2	(0.00)	0.30	(0.30)	(0.01)	3.75	(3.76)	Delay in the approval and release of funds impacting the initially planned cash flow	Accelerate the evaluation of technical-economic proposals	Non-critical	(3.76)						
Maintenance	Ball Mill 02 Components Puchase	(0.00)	-	(0.00)	0.00	4.00	(4.00)	Project deferred to 2027	Formalize the deferral according to the change management procedure	Non-critical			(4.00)				
Maintenance	Shovel P&P 4100 Comp 2025-2027	2.89	-	2.89	3.21	-	3.21	Acceleration in the procurement of major components	-	Non-critical		3.21					
Maintenance	Truck CAT 797F Comp 2025-2027	-	1.50	(1.50)	-	3.00	(3.00)	Delay in the arrival of components	Present a recovery plan in coordination with the Supply team	Non-critical		(3.00)					
Maintenance	Drill Electric Cat MD6640 Comp 2025-2027	0.31	1.32	(1.01)	0.31	1.32	(1.01)	Purchase orders in progress	Present a recovery plan in coordination with the Supply team	Non-critical			(1.01)				
Maintenance	Shovel CAT 6060 Comp 2025-2027	0.22	3.30	(3.08)	0.63	3.75	(3.12)	Rescheduling of component delivery to Sep-26	Present a recovery plan in coordination with the Supply team	Non-critical			(3.12)				
Maintenance	Truck KOM 930E Comp 2025-2027	6.62	3.28	3.33	7.73	5.15	2.58	Acceleration in the procurement of major components	-	Non-critical		2.58					
Maintenance	Truck KOM 980E Comp 2025-2027	2.90	0.50	2.40	2.90	0.50	2.40	Acceleration in the procurement of major components	-	Non-critical		2.40					
Technical Services	Dewatering Pit FB & CB 2025	0.36	0.33	0.03	0.71	1.99	(1.28)	Delays in the procurement and delivery of piping.	Present a recovery plan in coordination with the Supply team	Non-critical		(1.28)					
Others	Acquisition of 4 Articulated Trucks	-	-	-	2.34	-	2.34	Originally scheduled for Sep-26	-	Non-critical			2.34				
	Main projects (US$ M)	**37.10**	**28.39**	**8.70**	**83.22**	**79.05**	**4.16**			**YTD (US$ M)**	**(3.76)**	**(4.93)**	**15.13**	**(2.28)**	**-**	**-**	**-**
	Total (US$ M)	**53.92**	**59.03**	**(5.10)**	**128.99**	**160.18**	**(31.18)**										

2026 Capex Execution

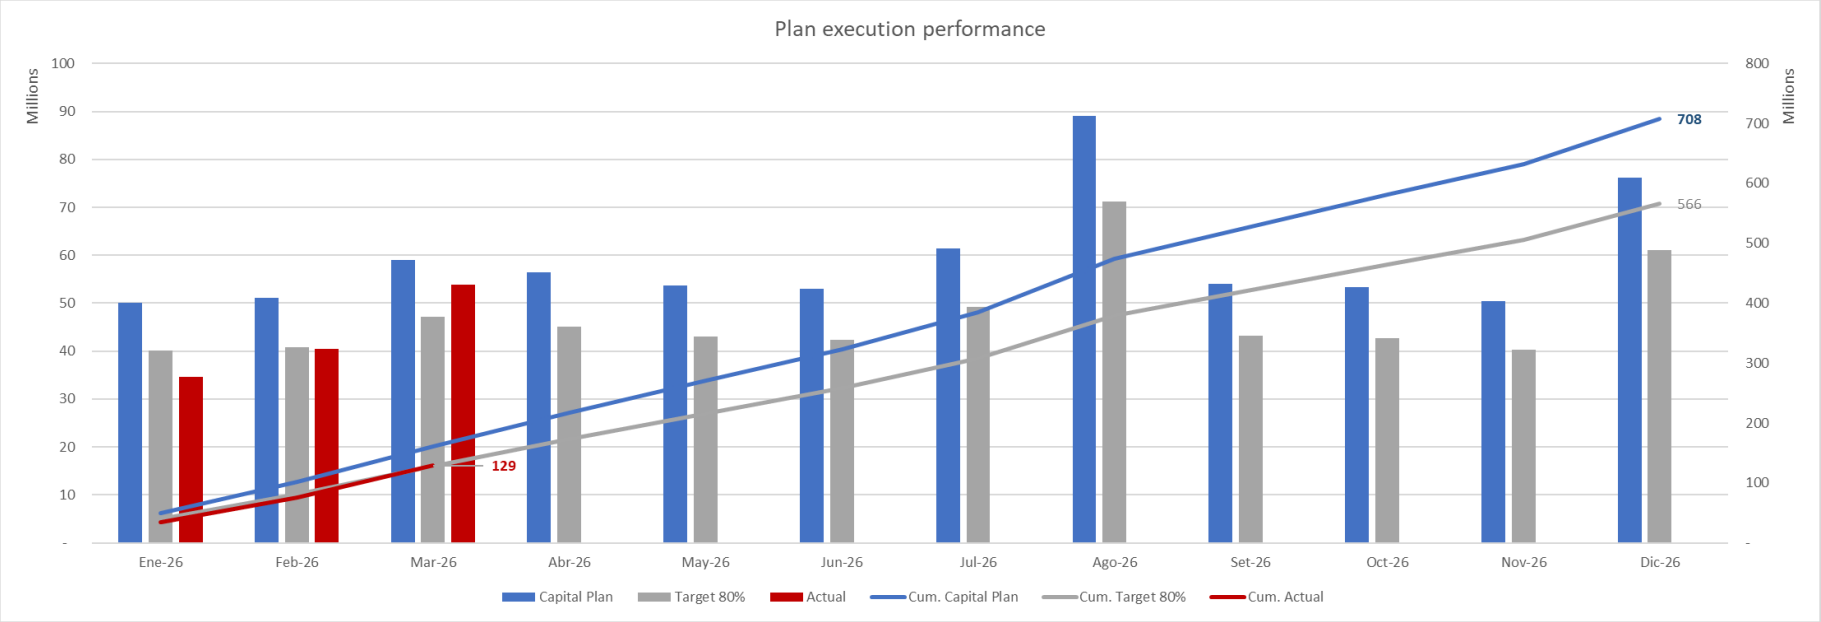

Total	Ene-26	Feb-26	Mar-26	Abr-26	May-26	Jun-26	Jul-26	Ago-26	Set-26	Oct-26	Nov-26	Dic-26
Performance based on Capital Plan	69.2%	79.1%	91.4%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
Cum. Performance	69.2%	74.2%	80.5%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%

Q1

Capex Portfolio Status / Studies

CAPEX Report 2026 - Studies (Mar-26)

Actual vs Capital Plan - 2026

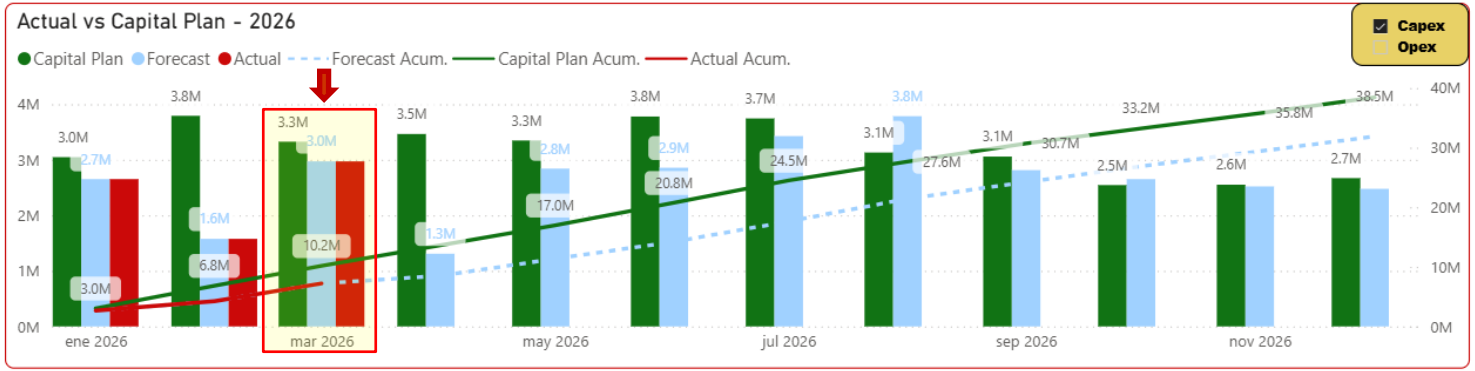

38.5M Capital Plan

31.9M Forecast

7.2M Actual to date

5.4M Open Commit

Summary by Projects to Mar-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Mar)	Act vs Prev. Fcst (Mar)
Plant Expansion 61 MTPY (FS)	Herman Aleman	1.39M	1.69M	1.69M	0.04M	0.47M
Pumps, thickeners&tanks optimization_FS	Herman Aleman	1.26M	0.12M	0.12M	-0.42M	-0.05M
Grinding pumping system optimization	Herman Aleman	1.19M	0.00M	0.00M	-0.40M	0.00M
Crusher Relocation (FS)	Herman Aleman	1.07M	2.14M	2.14M	0.39M	0.65M
Moly Plant Optimization (FS)	Herman Aleman	0.53M	0.14M	0.14M	-0.01M	0.10M
Pionero Waste Dump (FS)	Herman Aleman	0.49M	0.06M	0.06M	0.05M	0.00M
Total		**10.16M**	**7.20M**	**7.20M**	**-0.35M**	**2.45M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Plant Expansion 61 MTPY (FS)	5.82M	5.82M	1.69M	4.13M	0.37M	3.76M
Pumps, thickeners&tanks optimization_FS	5.03M	4.56M	0.12M	4.91M	0.01M	4.90M
Grinding pumping system optimization	4.75M	0.00M	0.00M	4.75M	0.81M	3.94M
Crusher Relocation (FS)	4.27M	4.27M	2.14M	2.13M	1.62M	0.51M
Moly Plant Optimization (FS)	3.00M	3.10M	0.14M	2.86M	0.27M	2.59M
Total	**38.45M**	**31.88M**	**7.20M**	**31.25M**	**102.48M**	

Goal for Abr-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Herman Aleman	Plant Expansion 61 MTPY (FS)	0.68M	0.12M
Herman Aleman	Pumps, thickeners&tanks optimization_FS	0.42M	0.03M
Herman Aleman	Grinding pumping system optimization	0.40M	0.00M
Herman Aleman	Crusher Relocation (FS)	0.36M	0.10M
Herman Aleman	Chalcobamba Feasibility	0.30M	0.00M
Herman Aleman	Moly Plant Optimization (FS)	0.26M	0.26M
Herman Aleman	New 3 1/2 " grinding ball Hopper - mill (FS)	0.22M	0.01M
Herman Aleman	Additional Tailings Storage (FS)	0.15M	0.46M
Marcela Insignares	Chalcobamba Shift Turnover	0.13M	0.01M
Herman Aleman	XP Camp Recovery & Expansion Ph1 (FS)	0.13M	0.07M
Herman Aleman	Thickeners Overflow Upgrade – Fifth pump	0.11M	0.00M
Total		**3.46M**	**1.31M**

Capex Portfolio Status / Implementation

CAPEX Report 2026 - Implementation (Mar-26)

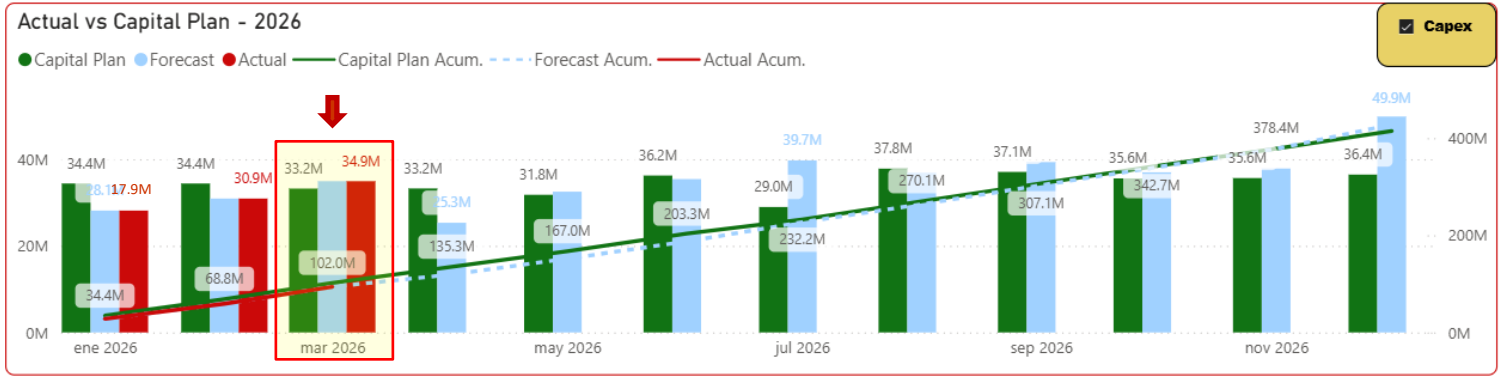

414.8M Capital Plan

427.8M Forecast

94.0M Actual to date

304.0M Open Commit

Summary by Projects to Mar-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Mar)	Act vs Prev. Fcst (Mar)
Pit FB Phase 6 - Infrastructure (IMP)	Reinaldo Ponce De León	14.19M	20.56M	20.56M	3.78M	2.31M
TD&RWI Pumping System (5&6)_Phase2 (IMP)	Alex Inostroza	12.81M	19.54M	19.54M	2.74M	1.13M
Tailings Dam Construction Stage VI (IMP)	Alex Inostroza	10.71M	10.82M	10.82M	0.72M	-0.30M
Chalcobamba 1 Sustaining	Reinaldo Ponce De León	9.98M	14.36M	14.36M	2.68M	1.86M
Pionero Waste Dump (IMP)	Reinaldo Ponce De León	9.62M	0.78M	0.78M	-2.54M	0.31M
Total		**102.01M**	**93.98M**	**93.98M**	**1.71M**	**5.90M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Pit FB Phase 6 - Infrastructure (IMP)	48.42M	60.79M	20.56M	27.86M	35.08M	
Chalcobamba 1 Sustaining	42.43M	51.02M	14.36M	28.06M	65.80M	
Tailings Dam Construction Stage VI (IMP)	39.14M	41.27M	10.82M	28.33M	119.18M	
Pionero Waste Dump (IMP)	38.49M	35.18M	0.78M	37.71M	1.08M	36.63M
TSF 1 - Stg VII / VIII Facilities (IMP)	37.72M	32.05M	0.00M	37.72M	0.07M	37.65M
Total	**414.81M**	**427.84M**	**93.98M**	**310.03M**	**397.39M**	

Goal for Abr-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Reinaldo Ponce De León	Pit FB Phase 6 - Infrastructure (IMP)	4.60M	4.80M
Alex Inostroza	TD&RWI Pumping System (5&6)_Phase2 (IMP)	4.33M	2.19M
Alex Inostroza	Column cells install. bulk flotat. (IMP)	3.39M	1.17M
Reinaldo Ponce De León	Chalcobamba 1 Sustaining	3.38M	4.93M
Reinaldo Ponce De León	Pionero Waste Dump (IMP)	3.21M	0.72M
Alex Inostroza	Tailings Dam Construction Stage VI (IMP)	3.17M	3.58M
Reinaldo Ponce De León	Pit FB Phase 6B - Infrastructure (IMP)	2.40M	2.47M
Alex Inostroza	FB BWM-Additional discharge point (IMP)	1.13M	0.05M
Total		**33.25M**	**25.32M**

Capex Portfolio Status / Land

CAPEX Report 2026 - Land (Mar-26)

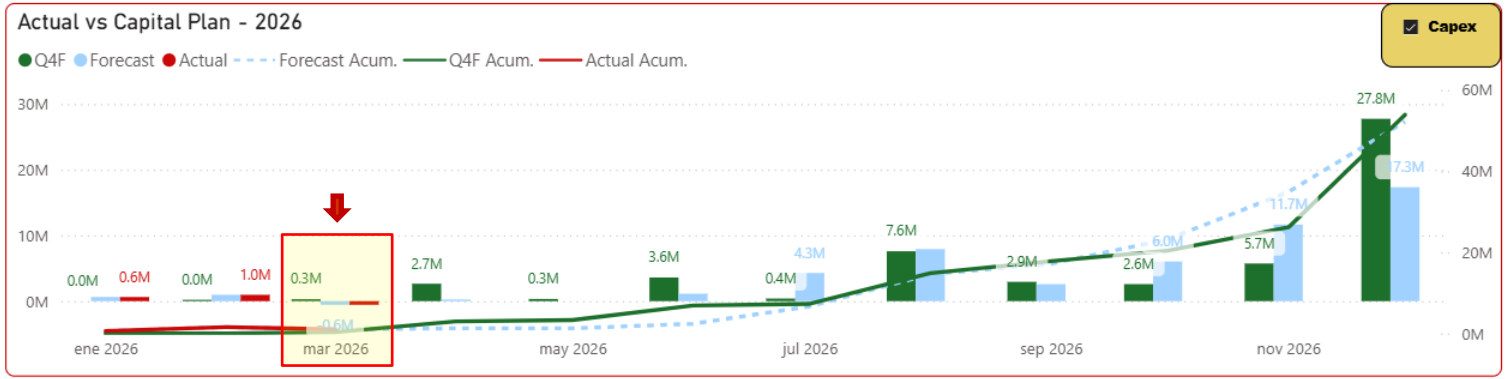

53.9M Capital Plan

52.2M Forecast

1.0M Actual to date

2.4M Open Commit

Summary by Projects to Mar-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Mar)	Act vs Prev. Fcst (Mar)
Socorro buffer land access	Gonzalo Garcia	0.30M	0.19M	0.19M	-0.25M	-0.10M
Social Liberation of Pumamarca(Sallahui)	Gonzalo Garcia	0.03M	-0.33M	-0.33M	-0.80M	-0.80M
"Triangulo" Land Purchase	Gonzalo Garcia	0.00M	0.00M	0.00M	0.00M	0.00M
Chalcobamba Land Access (Hancochiri)	Gonzalo Garcia	0.00M	0.00M	0.00M	0.00M	0.00M
FB Phase 7 Buffer Area Access	Gonzalo Garcia	0.00M	0.00M	0.00M	0.00M	0.00M
Total		**0.33M**	**1.03M**	**1.03M**	**-0.86M**	**-0.71M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
TSF2 Land Access (Communities)	11.45M	11.45M	0.00M	11.45M	0.00M	11.45M
TSF2 Land Access (Private Properties)	10.78M	10.78M	1.06M	9.71M	0.65M	9.06M
Chalcobamba Land Access (Hancochiri)	10.73M	0.00M	0.00M	10.73M	0.32M	10.41M
Stg3 - Sulfobamba Land Access	10.30M	10.30M	0.00M	10.30M	0.02M	10.29M
"Triangulo" Land Purchase	5.25M	5.25M	0.00M	5.25M	0.04M	5.21M
Total	**53.92M**	**52.23M**	**1.03M**	**52.89M**	**3.14M**	**49.75M**

Goal for Abr-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Gonzalo Garcia	TSF2 Land Access (Communities)	2.29M	0.00M
Gonzalo Garcia	Socorro buffer land access	0.30M	0.13M
Gonzalo Garcia	Stg3 - Sulfobamba Land Access	0.03M	0.00M
Gonzalo Garcia	Social Liberation of Pumamarca(Sallahui)	0.03M	0.00M
Gonzalo Garcia	"Triangulo" Land Purchase	0.00M	0.00M
Gonzalo Garcia	Chalcobamba Land Access (Hancochiri)	0.00M	0.00M
Gonzalo Garcia	FB Phase 7 Buffer Area Access	0.00M	0.00M
Gonzalo Garcia	Huañaculla Land Access	0.00M	0.03M
Augusto Cavero	New access and checkpoint -North area	0.00M	0.00M
Gonzalo Garcia	Social Access to Socorro Land – Conveyor	0.00M	0.00M
Gonzalo Garcia	TSF2 Land Access (Private Properties)	0.00M	0.09M
Total		**2.65M**	**0.25M**

Capex Portfolio Status / Resource Development

CAPEX Report 2026 - Resource Development (Mar-26)

Actual vs Capital Plan - 2026

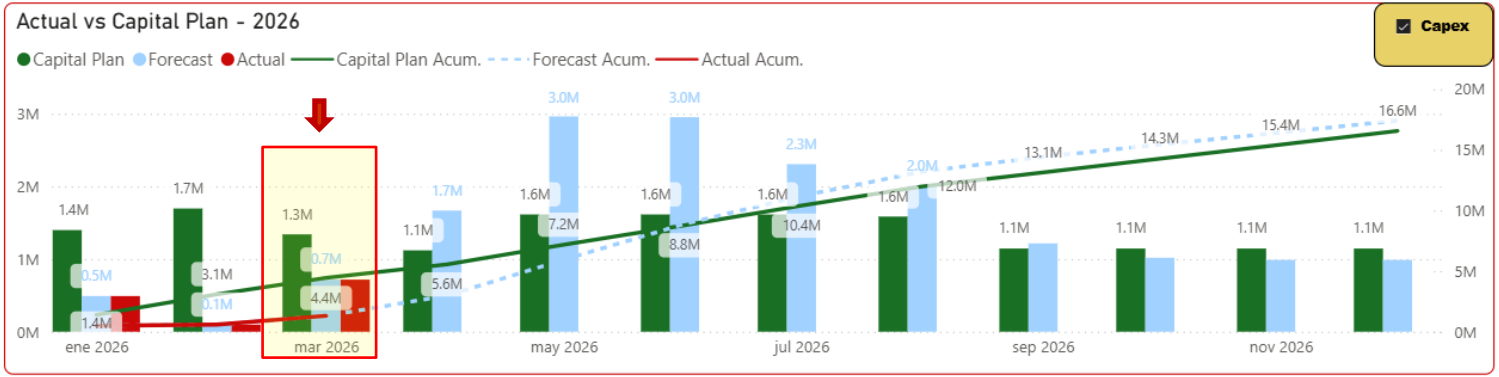

16.6M Capital Plan

16.9M Forecast

1.3M Actual to date

2.6M Open Commit

Summary by Projects to Mar-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Mar)	Act vs Prev. Fcst (Mar)
2025 CB SW Reserve Definition Drilling	Cesar Aguirre	2.01M	0.57M	0.57M	-0.64M	0M
2025-2026 FB Pit Reserve Def. Drilling	Cesar Aguirre	1.41M	0.11M	0.11M	-0.09M	0M
2021-22 CB Pit Reserve Definition Drilling	Cesar Aguirre	1.02M	-0.01M	-0.01M	-0.17M	0M
2021-22 CB SW Reserve Definition Drilling	Cesar Aguirre	0.00M	0.01M	0.01M	0.00M	0M
2023-2024 FB Pit Reserve Def. Drilling	Cesar Aguirre	0.00M	0.00M	0.00M	0.00M	0M
Total		**4.44M**	**1.31M**	**1.31M**	**-0.62M**	**0M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
2026-2027 CB Pit Reserve Definition Drilling	9.16M	9.16M	0.24M	8.92M	0.18M	8.75M
2025-2026 FB Pit Reserve Def. Drilling	3.72M	3.72M	0.11M	3.61M	1.20M	2.41M
2025 CB SW Reserve Definition Drilling	2.66M	2.66M	0.57M	2.09M	0.23M	1.86M
2021-22 CB Pit Reserve Definition Drilling	1.02M	1.02M	-0.01M	1.03M	0.67M	0.36M
2021-22 CB SW Reserve Definition Drilling	0.00M	0.20M	0.01M	-0.01M	0.16M	
Total	**16.56M**	**17.42M**	**1.31M**	**15.26M**	**2.56M**	**12.69M**

Goal for Abr-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Cesar Aguirre	2025 CB SW Reserve Definition Drilling	0.65M	0.13M
Cesar Aguirre	2025-2026 FB Pit Reserve Def. Drilling	0.47M	0.23M
Cesar Aguirre	2021-22 CB Pit Reserve Definition Drilling	0.00M	0.17M
Cesar Aguirre	2021-22 CB SW Reserve Definition Drilling	0.00M	0.06M
Cesar Aguirre	2024-2025 FB Pit Reserve Def. Drilling	0.00M	0.09M
Cesar Aguirre	2026-2027 CB Pit Reserve Definition Drilling	0.00M	0.99M
Total		**1.12M**	**1.67M**

Capex Portfolio Status / Maintenance

CAPEX Report 2026 - Maintenance (Mar-26)

Actual vs Capital Plan - 2026

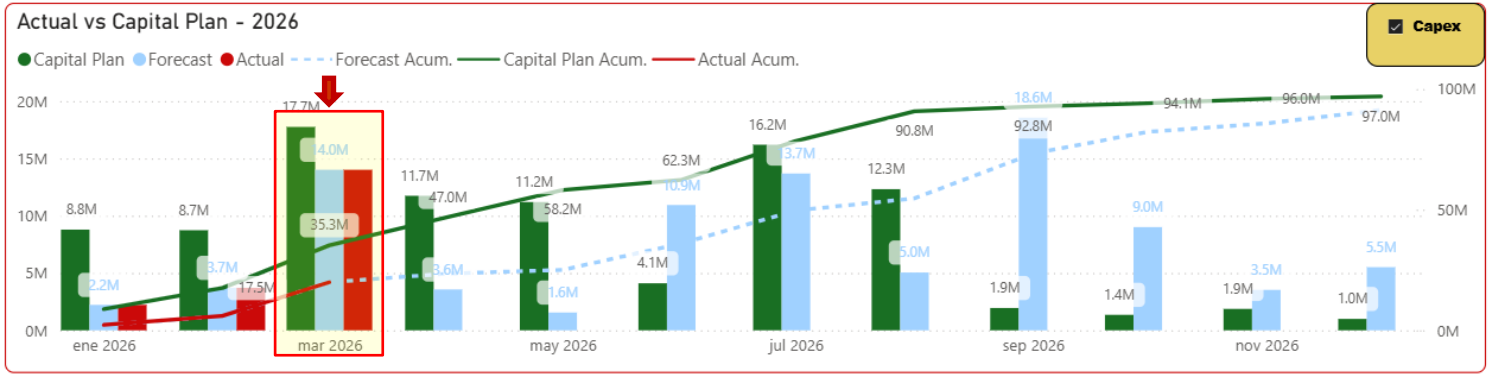

97.0M Capital Plan

91.3M Forecast

19.9M Actual to date

58.9M Open Commit

Summary by Projects to Mar-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Mar)	Act vs Prev. Fcst (Mar)
Overland Conveyor 4 Replacement 2025	Hugo Albuqueque	5.32M	4.25M	4.25M	-0.54M	1M
Truck KOM 930E Comp 2025-2027	Jimmy Ortiz	5.15M	7.73M	7.73M	3.33M	7M
Ball Mill 02 Components Puchase	Hugo Albuqueque	4.00M	0.00M	0.00M	0.00M	0M
Shovel CAT 6060 Comp 2025-2027	Jimmy Ortiz	3.75M	0.63M	0.63M	-3.08M	0M
Truck CAT 797F Comp 2025-2027	Jimmy Ortiz	3.00M	0.00M	0.00M	-1.50M	0M
Total		**35.27M**	**19.94M**	**19.94M**	**-3.74M**	**14M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Truck KOM 930E Comp 2025-2027	16.49M	15.48M	7.73M	8.76M	7.74M	1.02M
Overland Conveyor 4 Replacement 2025	8.87M	6.25M	4.25M	4.62M	1.24M	3.38M
Truck CAT 797F Comp 2025-2027	7.28M	7.08M	0.00M	7.28M	16.94M	
Shovel P&P 4100 Comp 2025-2027	6.87M	7.04M	3.21M	3.66M	5.02M	
Shovel overhaul 2 P&H 41000 (SH003/S0004	6.48M	6.93M	-8.88E-16	6.48M	0.04M	6.45M
Total	**96.98M**	**91.31M**	**19.94M**	**77.05M**	**58.92M**	**18.13M**

Goal for Abr-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Jimmy Ortiz	Truck KOM 980E Comp 2025-2027	2.55M	0.00M
Hugo Albuqueque	Overland Conveyor 4 Replacement 2025	1.77M	1.40M
Jimmy Ortiz	Drilling overhaul Epiroc PV351 (TD009)	1.00M	0.00M
Jimmy Ortiz	Truck KOM 930E Comp 2025-2027	1.00M	0.90M
Jimmy Ortiz	Shovel overhaul 2 P&H 41000 (SH003/S0004	0.95M	0.37M
Jimmy Ortiz	Truck CAT 797F Comp 2025-2027	0.95M	0.00M
Jimmy Ortiz	Shovel Electric Cat 7495 Comp 2022-2024	0.66M	0.00M
Hugo Albuqueque	FB - CB Primary Crushing	0.57M	0.00M
Hugo Albuqueque	CRG001 Components Purchase	0.45M	0.00M
Jimmy Ortiz	Drilling overhaul P&H 320XPC (TD004)	0.45M	0.00M
Jimmy Ortiz	Drill Epiroc VP351D Comp 2025-2027	0.43M	0.00M
Hugo Albuqueque	Overland Conveyor 3 Replacement LoA	0.38M	0.00M
Total		**11.74M**	**3.57M**

Capex Portfolio Status / Technical Services

CAPEX Report 2026 - Technical Services (Mar-26)

Actual vs Capital Plan - 2026

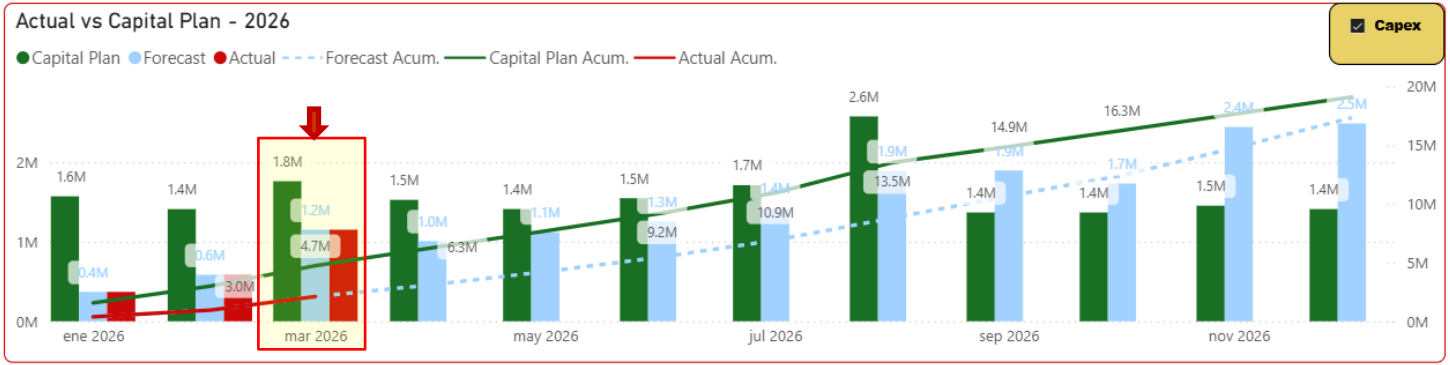

19.1M Capital Plan

17.4M Forecast

2.1M Actual to date

9.0M Open Commit

Summary by Projects to Mar-26

Name	P. Manager	Capital Plan	Act (YTD)	Act vs CP (Mar)	Act vs Prev. Fcst (Mar)
Dewatering Pit FB & CB 2025	Herminio Nieto	1.99M	0.71M	0.03M	0.03M
Dewatering Pit Program (FB, CB, etc)	Herminio Nieto	1.27M	0.00M	-1.08M	0.00M
2025-2026 Geotechnical Drilling FB	David Ojeda	0.88M	0.22M	-0.26M	-0.02M
Return of FB pit dewatering to East Chan	Herminio Nieto	0.60M	0.86M	0.42M	0.17M
2022 Ferrobamba PIT & Waste Dam Geotech	David Ojeda	0.00M	0.00M	0.00M	0.00M
Total		**4.74M**	**2.11M**	**-0.61M**	**0.46M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Dewatering Pit Program (FB, CB, etc)	11.00M	0.00M	0.00M	11.00M	0.00M	11.00M
Dewatering Pit FB & CB 2025	4.53M	2.60M	0.71M	3.82M	2.34M	1.48M
Return of FB pit dewatering to East Chan	2.59M	2.76M	0.86M	1.73M	1.74M	
2025-2026 Geotechnical Drilling FB	1.00M	1.00M	0.22M	0.78M	0.28M	0.50M
2022 Ferrobamba PIT & Waste Dam Geotech	0.00M	0.00M	0.00M	0.00M	0.01M	
Total	**19.12M**	**17.36M**	**2.11M**	**17.02M**	**9.04M**	**7.97M**

Goal for Abr-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Herminio Nieto	Dewatering Pit Program (FB, CB, etc)	1.08M	0.00M
Herminio Nieto	Dewatering Pit FB & CB 2025	0.33M	0.15M
David Ojeda	2025-2026 Geotechnical Drilling FB	0.12M	0.11M
David Ojeda	2022 Ferrobamba PIT & Waste Dam Geotech	0.00M	0.00M
Herminio Nieto	Dewatering Pit FB & CB 2026	0.00M	0.35M
Herminio Nieto	Dewatering Pit Ferrobamba 2024	0.00M	0.00M
David Ojeda	FB Microseismic Control	0.00M	0.00M
David Ojeda	FB-CB Geotechnical Drilling 2025@2038	0.00M	0.00M
Herminio Nieto	Return of FB pit dewatering to East Chan	0.00M	0.40M
Total		**1.53M**	**1.01M**

Capex Portfolio Status / Others

CAPEX Report 2026 - Others (Mar-26)

Actual vs Capital Plan - 2026

Capital Plan · Forecast · Actual · Forecast Acum. · Capital Plan Acum. · Actual Acum.

Capex / Opex

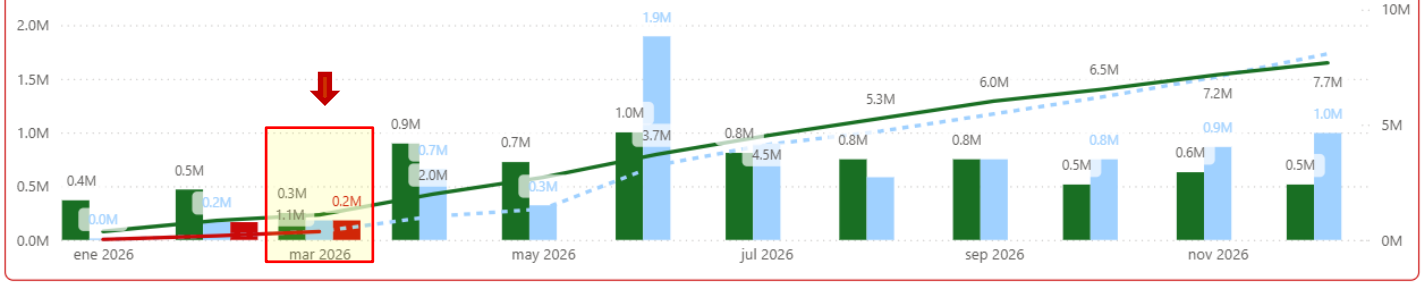

7.7M	Capital Plan
8.1M	Forecast
0.4M	Actual to date
0.8M	Open Commit

Summary by Projects to Mar-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Mar)	Act vs Prev. Fcst (Mar)
Process Water Improvement (FS)	Jean Vilchez	0.31M	0.10M	0.10M	-0.02M	0.00M
Digital Operation Control Centre	Abdon Guillen	0.30M	0.00M	0.00M	0.00M	0.00M
Paving of 13 Sections APU-CUZ road	Fernando Salinas	0.25M	0.00M	0.00M	-0.08M	-0.08M
FB BWM-FB & Huancarane (FS)	Jean Vilchez	0.18M	0.24M	0.24M	0.07M	0.00M
LB Centralization of fire alarms	Henry Delgado	0.05M	0.01M	0.01M	-0.05M	0.00M
Total		**1.09M**	**0.36M**	**0.36M**	**-0.07M**	**-0.96M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Huancuire Agreement (Phase 2)	3.64M	3.47M	0.00M	3.64M	0.00M	3.64M
Paving of 13 Sections APU-CUZ road	1.30M	1.30M	0.00M	1.30M	0.00M	1.30M
Selenium treatment plant (FS)	0.94M	0.94M	0.00M	0.94M	0.00M	0.94M
Process Water Improvement (FS)	0.51M	0.51M	0.10M	0.41M	0.00M	0.41M
Camps for Public Safety - HHR Wincho&Con	0.46M	0.42M	0.00M	0.46M	0.42M	0.03M
Total	**7.69M**	**8.08M**	**0.36M**	**7.33M**	**0.85M**	**6.48M**

Goal for Abr-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Augusto Cavero	Camps for Public Safety - HHR Wincho&Con	0.40M	0.00M
Jean Vilchez	Process Water Improvement (FS)	0.20M	0.31M
Jose Maticorena	Huancuire Agreement (Phase 2)	0.17M	0.00M
Fernando Salinas	Paving of 13 Sections APU-CUZ road	0.08M	0.00M
Henry Delgado	LB Centralization of fire alarms	0.03M	0.00M
Jean Vilchez	FB BWM-FB & Huancarane (FS)	0.01M	0.28M
Marcos Cocas	Access to Haquira route	0.00M	0.00M
Marcos Cocas	Access to Inquilpata route	0.00M	0.00M
Abdon Guillen	Digital Operation Control Centre	0.00M	0.00M
Jean Vilchez	Ferrobamba Basin Water Management (FS)	0.00M	0.08M
Fernando Salinas	Heavy Haul Road 02 Bridges Reinforcement	0.00M	0.00M
Total		**0.90M**	**0.66M**

Opex Development

Opex Portfolio Status

OPEX Report 2026 (As of Mar-26)

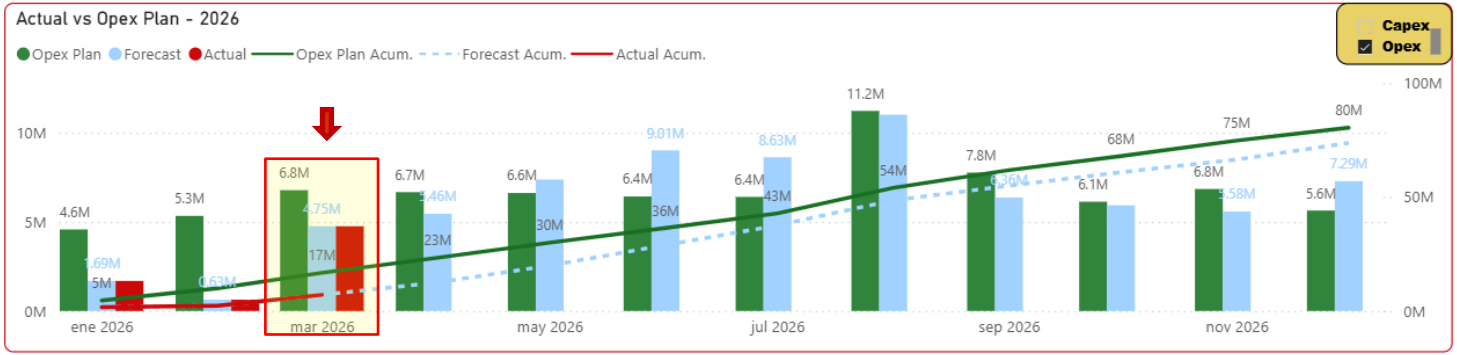

80.4M	Opex plan
73.7M	Forecast
16.7M	YTD (OP)
7.1M	Actual to date
24.0M	Open Commit

Summary by Areas (YTD)



Summary by Areas with Year To Go 2026

Grupo	Opex Plan	Forecast	Actual	YTG (OP)	O. Comm.	New Comm.
Studies	59.79M	54.52M	5.06M	54.73M	14.55M	40.18M
Logistic	12.65M	12.79M	1.13M	11.52M	4.98M	6.55M
Permits	7.02M	5.86M	0.85M	6.17M	4.08M	2.09M
Others	0.94M	0.54M	0.04M	0.91M	0.34M	0.56M
Total	**80.41M**	**73.71M**	**7.07M**	**73.34M**	**23.96M**	**49.39M**

Status for Mar-26

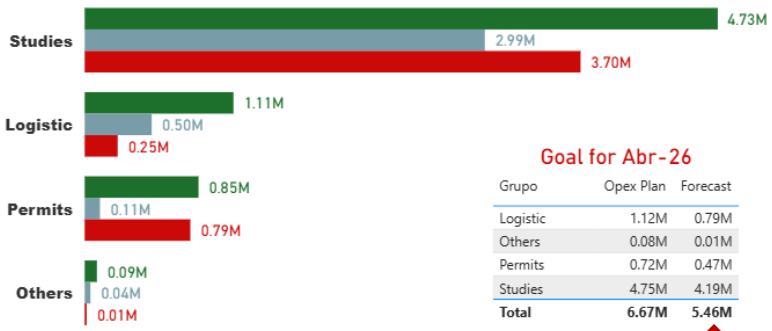

Goal for Abr-26

Grupo	Opex Plan	Forecast
Logistic	1.12M	0.79M
Others	0.08M	0.01M
Permits	0.72M	0.47M
Studies	4.75M	4.19M
Total	**6.67M**	**5.46M**

* Previous forecast

Opex Portfolio Status / Studies

OPEX Report 2026 - Studies (Mar-26)

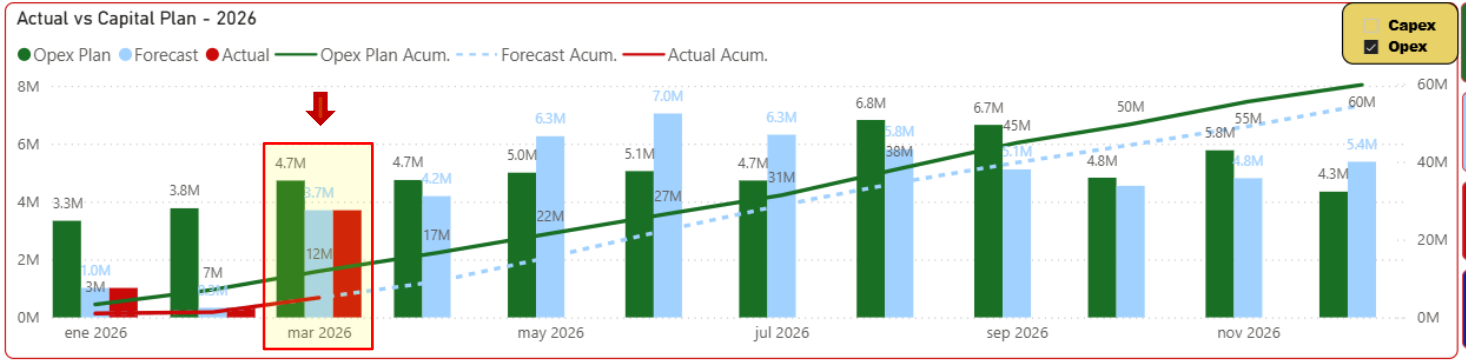

59.8M Opex plan

54.5M Forecast

5.1M Actual to date

14.6M Open Commit

Summary by Projects (YTD)

Name	Opex Plan	Forecast	Act to date	Act vs OP (Mar)	Act vs Prev. Fcst (Mar)
Tailings Storage Facility 2 PFS	4.42M	2.54M	2.54M	-0.42M	-0.11M
Ampliacion Planta 81 MTPY	3.90M			-1.28M	
Selenium treatment plant (PFS)	1.09M	0.44M	0.44M	0.14M	-0.22M
FB Underground (SC)	0.81M	0.15M	0.15M	-0.22M	-0.02M
Material Movement/Hybrid trucks(PFS)	0.79M	0.00M	0.00M	-0.56M	0.00M
Total	**11.84M**	**5.06M**	**5.06M**	**-1.02M**	**0.72M**

Summary by Projects with Year To Go 2026

Name	Opex Plan	Forecast	Actual	YTG	O.Comm.	New Comm.
Tailings Storage Facility 2 PFS	21.20M	19.59M	2.54M	18.65M	10.56M	8.09M
Ampliacion Planta 81 MTPY	15.61M			15.61M	0.13M	15.48M
FB Underground (SC)	7.41M	3.37M	0.15M	7.26M	0.20M	7.06M
Reposicion Chalcobamba (SC)	5.14M	17.30M	0.90M	4.25M	0.82M	3.42M
Material Movement/Hybrid trucks(PFS)	4.68M	1.16M	0.00M	4.68M	1.63M	3.06M
Sulfobamba PFS	2.83M	2.66M	0.26M	2.57M	0.29M	2.28M
Total	**59.79M**	**54.52M**	**5.06M**	**54.73M**	**14.55M**	**40.18M**

Goal for Abr-26

Project Manager / Study Lead	Name	Opex Plan	Forecast
Yessenia Granados	Tailings Storage Facility 2 PFS	2.09M	1.10M
Herman Aleman	Ampliacion Planta 81 MTPY	1.11M	
Marcos Cocas	FB Underground (SC)	0.73M	0.05M
Marcela Insignares	Material Movement/Hybrid trucks(PFS)	0.21M	0.00M
Marcos Cocas	Reposicion Chalcobamba (SC)	0.20M	2.19M
Jean Vilchez	Selenium treatment plant (PFS)	0.15M	0.60M
Marcos Cocas	Sulfobamba PFS	0.15M	
Yessenia Granados	Additional Tailings Storage PFS	0.09M	0.01M
Total		**4.75M**	**4.19M**

Opex Portfolio Status / Logistic

OPEX Report 2026 - Logistic (Mar-26)

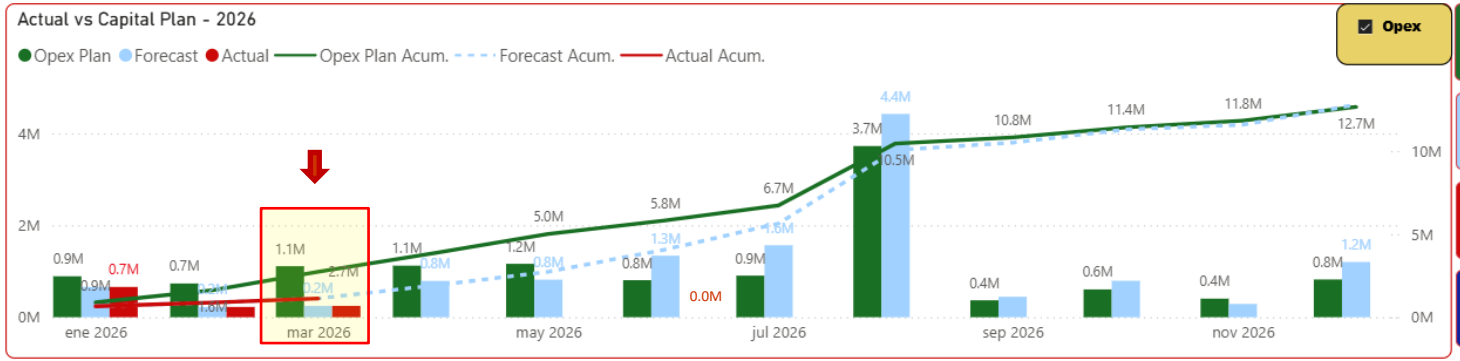

12.7M Opex plan

12.8M Forecast

0.7M Actual to date

5.0M Open Commit

Summary by Projects (YTD)

Name	Opex Plan	Forecast	Act to date	Act vs OP (Mar)	Act vs Prev. Fcst (Mar)
Ing. Vias nacionales(Cusco-Apurimac)	1.90M	0.94M	0.94M	-0.54M	-0.17M
Logistic Options PFS - Roads (Monitoreos 2020 / Ing 2021)	0.33M	0.19M	0.19M	-0.05M	-0.08M
LB-Exit Routes	0.30M	0.00M	0.00M	-0.10M	0.00M
Logistic Options PFS - Pipeline	0.11M	0.00M	0.00M	-0.11M	0.00M
Train LB-Marcona	0.06M	0.00M	0.00M	0.06M	0.00M
Total	**2.74M**	**1.13M**	**1.13M**	**-0.86M**	**-0.25M**

Summary by Projects with Year To Go 2026

Name	Opex Plan	Forecast	Actual	YTG	O.Comm.	New Comm.
Ing. Vias nacionales(Cusco-Apurimac)	4.76M	4.76M	0.94M	3.82M	4.28M	
Route LB-Haquira-Izcahuaca-Marcona	3.32M	3.32M	0.00M	3.32M	0.00M	3.32M
Logistic Options PFS - Roads (Monitoreos 2020 / Ing 2021)	2.34M	2.47M	0.19M	2.15M	0.69M	1.45M
LB-Exit Routes	1.21M	1.21M	0.00M	1.21M	0.00M	1.21M
Logistic Options PFS - Pipeline	0.53M	0.53M	0.00M	0.53M	0.00M	0.53M
Total	**12.65M**	**12.79M**	**1.13M**	**11.52M**	**4.98M**	**6.55M**

Goal for Abr-26

Project Manager / Study Lead	Name	Opex Plan	Forecast
Robert Villanueva	Ing. Vias nacionales(Cusco-Apurimac)	0.91M	0.46M
Marcos Cocas	LB-Exit Routes	0.10M	0.00M
Marcos Cocas	Logistic Options PFS - Roads (Monitoreos 2020 / Ing 2021)	0.10M	0.33M
Marcos Cocas	Route LB-Haquira-Izcahuaca-Marcona	0.01M	0.00M
Total		**1.12M**	**0.79M**
