Portfolio Report

- Capex LB
- Opex Development

Feb- 2026

Contenido

1. Portafolio Capex
   - Capex por Areas
   - Forecast Mar-2026 por Areas y Responsables / Capex
2. Portafolio Opex Development & Resource Development
   - Opex por Areas
   - Forecast Mar-2026 por Areas y Responsables / Opex

LB Capex

Capex Portfolio Status

CAPEX Report 2026 (As of Feb-26)

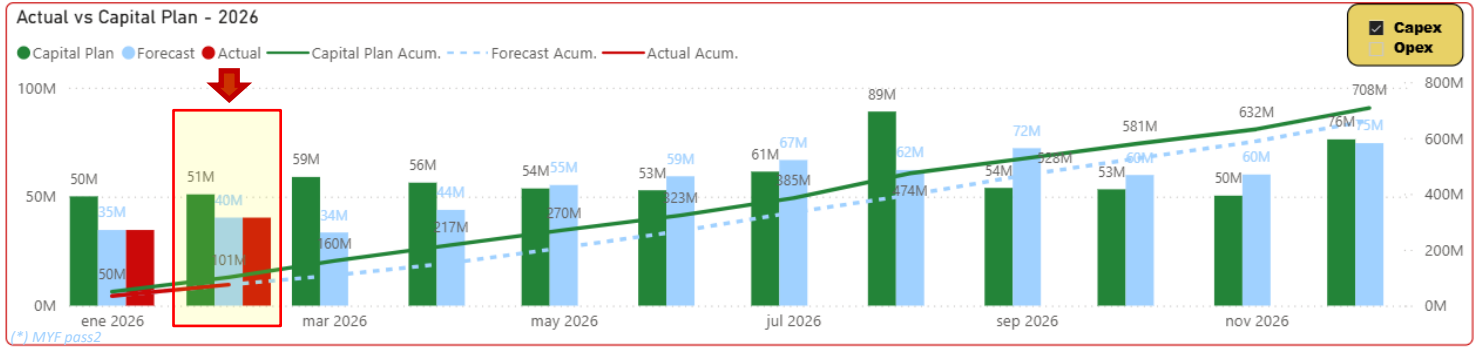

707.8M	Capital Plan
663.0M	Forecast
101.1M	YTD (CP)
75.1M	Actual to date
428.0M	Open Commit

Summary by Areas (YTD)









Summary by Areas with Year To Go 2026

N°	Grupo	Capital Plan	Forecast	Actual	YTG (CP)	O. Comm.	New Comm.
1	Studies	38.45M	34.29M	4.23M	34.22M	6.42M	27.81M
2	Implementation	414.81M	418.51M	59.04M	355.76M	335.21M	20.56M
3	Others	184.01M	139.49M	9.61M	174.40M	82.26M	92.14M
4	Resource Development	16.56M	17.68M	0.59M	15.97M	1.06M	14.91M
5	Land	53.92M	53.01M	1.59M	52.33M	3.03M	49.31M
Total		**707.75M**	**662.98M**	**75.06M**	**632.70M**	**427.98M**	**204.72M**

Status for Feb-26

Goal for Mar-26

Grupo	Capital Plan	Forecast
Implementation	33.22M	29.75M
Land	0.30M	0.15M
Others	20.84M	1.25M
Resource Development	1.34M	0.98M
Studies	3.33M	1.43M
Total	**59.03M**	**33.56M**

* Previous forecast

Capex Portfolio Status / Desviations by Area / Feb-26 Results

Capital completion rate :

	≥ 80%
	75% ≤ r < 80%
	< 75%

Group	Executed by	Budget	Actual Feb-26	Budget Feb-26	Var Feb-26	Actual YTD	Budget YTD	Var YTD	Budget Mar-26
Project Delivery	DevelopStudies	38.5	1.6	3.8	-2.2	4.2	6.8	-2.6	3.3
	ProjectDelivery	414.8	30.9	34.4	-3.5	59.1	68.8	-9.7	33.2
Resource Development	ResourceDevelopm	16.6	0.1	1.7	-1.6	0.6	3.1	-2.5	1.3
Land Access	LandAccess	53.9	1.0	0.0	0.9	1.6	0.0	1.6	0.3
Mine Operation & Others	Maintenance	97.0	3.7	8.7	-5.0	5.9	17.5	-11.6	17.7
	MineOper	45.0	2.3	0.2	2.1	2.5	0.5	2.0	0.6
	TechServices	19.1	0.6	1.4	-0.8	1.0	3.0	-2.0	1.8
	Logistics	1.3	0.0	0.1	-0.1	0.0	0.2	-0.2	0.1
	IT-TechServ	13.6	0.0	0.3	-0.2	0.0	0.4	-0.3	0.5
	ConcentPlant	1.6	0.0	0.0	0.0	0.0	0.2	-0.2	0.0
	StrategPlan	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	SHE	0.1	0.0	0.0	0.0	0.0	0.0	0.0	0.1
	Water&Tailings	1.7	0.2	0.1	0.1	0.2	0.4	-0.2	0.1
	CCRR	3.6	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	Others	0.9	0.0	0.3	-0.3	0.0	0.3	-0.3	0.0
	Total US$M	**707.8**	**40.4**	**51.0**	**-10.7**	**75.1**	**101.1**	**-26.1**	**59.0**

2026 Capex Execution

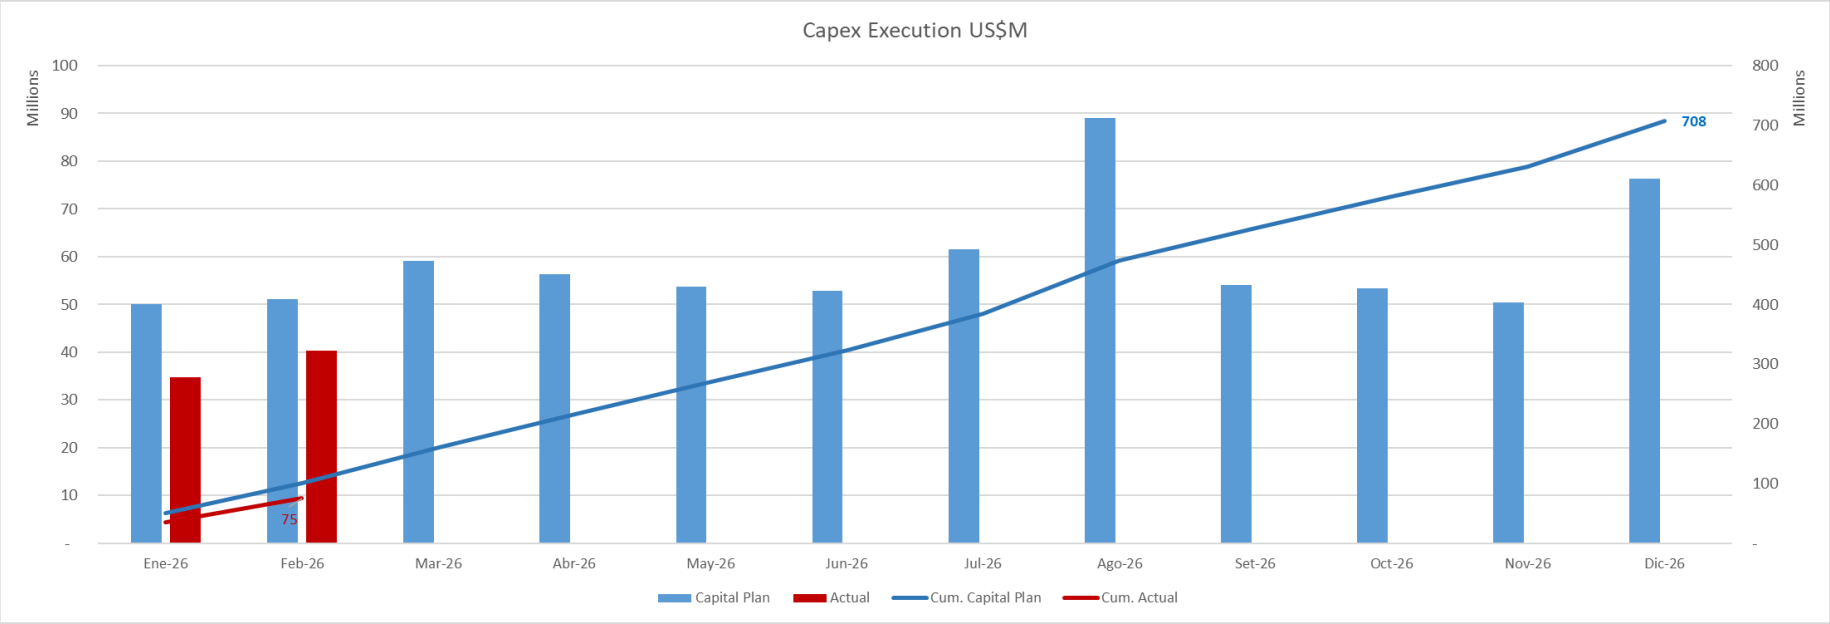

Total	Ene-26	Feb-26	Mar-26	Abr-26	May-26	Jun-26	Jul-26	Ago-26	Set-26	Oct-26	Nov-26	Dic-26
Performance based on Capital Plan	69.2%	79.1%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
Cum. Performance	69.2%	74.2%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%

Capex Portfolio Status / Main desviations – Top 10 Projects / Feb-26 Results

Code	Project	Executed by	YTD		
			Actual	BUD	Var
5200P-015842	Pionero Waste Dump (IMP)	PD + Mine Operations	0.11	6.42	▼ (6.30)
5200P-015816	Ball Mill 02 Components Puchase	Maintenance	0.00	4.00	▼ (3.99)
5200P-017133	DMO Ferro 2	ProjectDelivery	-	3.45	▼ (3.46)
5200P-016375	Foaming excess control in flotation	ProjectDelivery	0.14	1.99	▼ (1.85)
5200P-015576	Drilling overhaul P&H 320XPC (TD003)	Maintenance	-	1.63	▼ (1.63)
5200P-016577	Truck CAT 797F Comp 2025-2027	Maintenance	-	1.50	▼ (1.50)
5200P-016993	Recovery of Grinding Box Drains (FS)	ProjectDelivery	0.04	1.36	▼ (1.32)
5200P-017042	Fifth Barge for Recovered Water System	ProjectDelivery	0.16	1.47	▼ (1.31)
5200P-017024	Dewatering Pit FB & CB 2025	TechServices	0.35	1.66	▼ (1.31)
5200P-016387	DMO Ferro 1	ProjectDelivery	0.04	1.27	▼ (1.23)
		Total US$M	**0.84**	**24.75**	▼ **(23.91)**

Capex Portfolio Status / Main desviations / Feb-26 Results

Studies -$2.2M

Code	Project	ACT	BUD	LAST FCAST	Var ACT vs BUD		Reason	Action
5200P-016562	Grinding pumping system optimization	-	0.40	-	▼	(0.40)	Project cancelled	-
5200P-017054	Pumps, thickeners&tanks optimization_FS	0.08	0.42	0.01	▼	(0.34)	FS completed. Implementation APF pending submission.	Submit Implementation APF.
5200P-017198	Dispersant Reagent Preparation Plant(FS)	0.02	0.39	-	▼	(0.36)	Cost optimization. Potencial savings.	Confirm savings

Project Delivery -$3.5M

Code	Project	ACT	BUD	LAST FCAST	Var ACT vs BUD		Reason	Action
5200P-015440	Chalcobamba 1 Sustaining	4.01	3.32	3.45	▲	0.69	Earthworks at Pond 3 originally scheduled for Apr-	
5200P-015468	TD&RWI Presurizzed Gravity_Phase1 (IMP)	0.48	-	0.55	▲	0.48		
5200P-015580	Pit FB Phase 6 - Infrastructure (IMP)	6.91	4.70	6.07	▲	2.21	Early procurement for electromechanical works.	
5200P-015754	TD&RWI Pumping System (5&6)_Phase2 (IMP)	6.72	4.10	5.80	▲	2.62	Early procurement for electrical components.	
5200P-015791	Tailings Dam Construction Stage VI (IMP)	2.39	3.95	2.50	▼	(1.56)	Lower backfill placement due to reduced "mine dispatch" in Feb-26: 1.57 KTN actual vs. 2.79 KTN planned.	Specific case. No deviations in the material delivery plan are expected
5200P-015842	Pionero Waste Dump (IMP)	0.03	3.21	0.48	▼	(3.18)	Delays in face release due to interference with existing infrastructure.	Prioritize finalizing the awarding processes.
5200P-016255	Pit FB Phase 6B - Infrastructure (IMP)	3.87	2.11	2.61	▲	1.76	Early earthworks at Ticona access.	
5200P-016326	FB BWM-Seepage&Huancarane to TSF-Se Cont	0.38	1.72	0.38	▼	(1.34)	Late start due to award delays.	Implement recovery plan with mitigation
5200P-016327	FB BWM-Additional discharge point (IMP)	0.05	0.81	0.06	▼	(0.75)	Delay in procurement and engineering processes.	Implement recovery plan with mitigation
5200P-016375	Foaming excess control in flotation	0.01	0.75	0.11	▼	(0.75)	Delay in engineering development and award.	Ensure that the prior engineering phase is
5200P-016387	DMO Ferro 1	-	0.58	0.04	▼	(0.58)	Delay due to engineering definition.	Project in the process of closing and already
5200P-016399	Column cells install. bulk flotat. (IMP)	4.20	3.21	3.54	▲	0.99	Recovery of delayed works	
5200P-016993	Recovery of Grinding Box Drains (FS)	0.03	0.46	0.46	▼	(0.44)		
5200P-017042	Fifth Barge for Recovered Water System	0.02	0.82	0.01	▼	(0.80)	Project in closing phase; pending settlement of claims with the main contractor.	Project in the process of closing
5200P-017133	DMO Ferro 2	0.01	1.71	-	▼	(1.71)	Delay in the approval and release of funds impacting the initially planned cash flow	Accelerate the evaluation of technical-economic proposals.
5200P-017256	Chalcobamba 2 - Ph1 (MEIA-4 / ITS-10/11)	0.06	0.42	0.05	▼	(0.35)		
5200P-017641	CVB-04 conveyor belt crossing drainage	-	0.72	-	▼	(0.72)	Procurement process delay	Accelerate the purchase of equipment
5200P-017717	CB1 Ph1 environmental & water management	0.64	-	-	▲	0.64		

Capex Portfolio Status / Main desviations / Feb-26 Results

Resource Development -$1.6M

Code	Project	ACT	BUD	LAST FCAST	Var ACT vs BUD	Reason	Action
5200P-013861	2024-26 CB Pit Reserve Definition Drilli	(0.08)	0.56	0.61	▼ (0.64)	Start-of-work rescheduled for late Feb-26	Resolve the issue with ECOSEM related to the availability of auxiliary equipment
5200P-016411	2025-2026 FB Pit Reserve Def. Drilling	0.05	0.47	0.28	▼ (0.42)		
5200P-017155	2025 CB SW Reserve Definition Drilling	0.09	0.67	0.59	▼ (0.58)	Start-of-work rescheduled for late Feb-26	Resolve the issue with ECOSEM related to the availability of auxiliary equipment

Maintenance -$5.0M

Code	Project	ACT	BUD	LAST FCAST	Var ACT vs BUD	Reason	Action
5200P-014913	Overland Conveyor 4 Replacement 2025	1.44	1.77	1.06	▼ (0.34)		
5200P-014914	Overland Conveyor 3 Replacement LoA	-	0.38	-	▼ (0.38)		
5200P-014916	FB - CB Primary Crushing	0.00	0.35	0.00	▼ (0.35)		
5200P-015576	Drilling overhaul P&H 320XPC (TD003)	-	1.03	-	▼ (1.03)	Savings planned to support the Business Case (drill replacement); otherwise, overhaul execution starts Aug-26.	Cancellation confirmation pending
5200P-015817	CRG001 Components Purchase	-	0.45	-	▼ (0.45)		
5200P-016574	Shovel CAT 6060 Comp 2025-2027	-	0.45	0.45	▼ (0.45)		
5200P-016576	Shovel P&P 4100 Comp 2025-2027	0.32	-	0.32	▲ 0.32		
5200P-016577	Truck CAT 797F Comp 2025-2027	-	1.50	-	▼ (1.50)	Sole-source award in progress; CAT 797F	In the purchasing process
5200P-016579	Truck KOM 930E Comp 2025-2027	1.12	1.87	1.12	▼ (0.75)	Delay in the arrival of components	Rescheduled for Mar-26

Capex Portfolio Status / Main desviations / Feb-26 Results

		Month			YTD				Factors under control				Uncertainty Factors		
Executed by	Project	Actual	Bud	Var	Actual	Bud	Var	Criticality	APF approval	Supply / Bidding process	Projects in Execution / Re schedulir	Projects under definition	Permits and access	Contracts with Communiti es	Land / CCRR / Negotiatio n proces
ProjectDelivery	Tailings Dam Construction Stage VI (IMP)	2.39	3.95	(1.56)	7.21	7.82	(0.62)	Non-critical			(0.62)				
ProjectDelivery	Pionero Waste Dump (IMP)	0.03	3.21	(3.18)	0.11	6.42	(6.30)	Critical		(6.30)					
ProjectDelivery	FB BWM-Seepage&Huancarane to TSF-Se Cont	0.38	1.72	(1.34)	1.53	2.56	(1.03)	Non-critical		(1.03)					
ProjectDelivery	FB BWM-Additional discharge point (IMP)	0.05	0.81	(0.75)	0.06	1.12	(1.07)	Non-critical		(1.07)					
ProjectDelivery	Foaming excess control in flotation	0.01	0.75	(0.75)	0.14	1.99	(1.85)	Non-critical		(1.85)					
ProjectDelivery	DMO Ferro 1	-	0.58	(0.58)	0.04	1.27	(1.23)	Non-critical				(1.23)			
ProjectDelivery	Fifth Barge for Recovered Water System	0.02	0.82	(0.80)	0.16	1.47	(1.31)	Non-critical			(1.31)				
ProjectDelivery	DMO Ferro 2	0.01	1.71	(1.71)	(0.00)	3.45	(3.46)	Non-critical	(3.46)						
ProjectDelivery	CVB-04 conveyor belt crossing drainage	-	0.72	(0.72)	-	0.72	(0.72)	Critical		(0.72)					
ResourceDevelopm	2024-26 CB Pit Reserve Definition Drilling	(0.08)	0.56	(0.64)	(0.04)	0.82	(0.86)	Non-critical		(0.86)					
ResourceDevelopm	2025 CB SW Reserve Definition Drilling	0.09	0.67	(0.58)	0.54	1.34	(0.80)	Non-critical		(0.80)					
Maintenance	Drilling overhaul P&H 320XPC (TD003)	-	1.03	(1.03)	-	1.63	(1.63)	Non-critical				(1.63)			
Maintenance	Truck CAT 797F Comp 2025-2027	-	1.50	(1.50)	-	1.50	(1.50)	Non-critical		(1.50)					
Maintenance	Truck KOM 930E Comp 2025-2027	1.12	1.87	(0.75)	1.12	1.87	(0.75)	Non-critical			(0.75)				
TechServices	Dewatering Pit FB & CB 2025	0.29	0.83	(0.54)	0.35	1.66	(1.31)	Non-critical			(1.31)				
	Main projects (US$ M)	**4.30**	**20.73**	**(16.43)**	**11.21**	**35.64**	**(24.44)**	**YTD (US$**	**(3.46)**	**(14.13)**	**(3.99)**	**(2.86)**	**-**	**-**	**-**
	Total (US$ M)	**40.37**	**51.03**	**(10.66)**	**75.07**	**101.15**	**(26.08)**								

Capex Portfolio Status / Desviations by Area / Mar-26 Forecast

Group	Executed by	Actual W1	BUD Mar-26	Latest Fcast Mar-26	Variation Latest Fcast vs BUD	
Project Delivery	DevelopStudies	0.45	3.33	1.43	▼	(1.90)
	ProjectDelivery	6.25	33.22	29.75	▼	(3.47)
Project Delivery Total		**6.70**	**36.55**	**31.17**	▼	(5.37)
Resource Development	ResourceDevelopm	0.01	1.34	0.98	▼	(0.36)
Resource Development Total		**0.01**	**1.34**	**0.98**	▼	(0.36)
Land Access	LandAccess	0.38	0.30	0.15	▼	(0.15)
Land Access Total		**0.38**	**0.30**	**0.15**	▼	(0.15)
Mine Operation & Others	CCRR	-	-	-		-
	ConcentPlant	-	-	-		-
	IT-TechServ	-	0.47	-	▼	(0.47)
	Logistics	-	0.08	0.08		-
	Maintenance	0.43	17.75	-	▼	(17.75)
	MineOper	-	0.61	-	▼	(0.61)
	Others	-	-	-		-
	SHE	-	0.05	-	▼	(0.05)
	TechServices	0.04	1.76	0.99	▼	(0.77)
	Water&Tailings	0.12	0.12	0.18	▲	0.06
Mine Operation & Others Total		**0.58**	**20.84**	**1.25**	▼	(19.59)
Grand Total US$M		**7.68**	**59.03**	**33.56**	▼	(25.47)

Capex Portfolio Status / Studies

CAPEX Report 2026 - Studies (Feb-26)

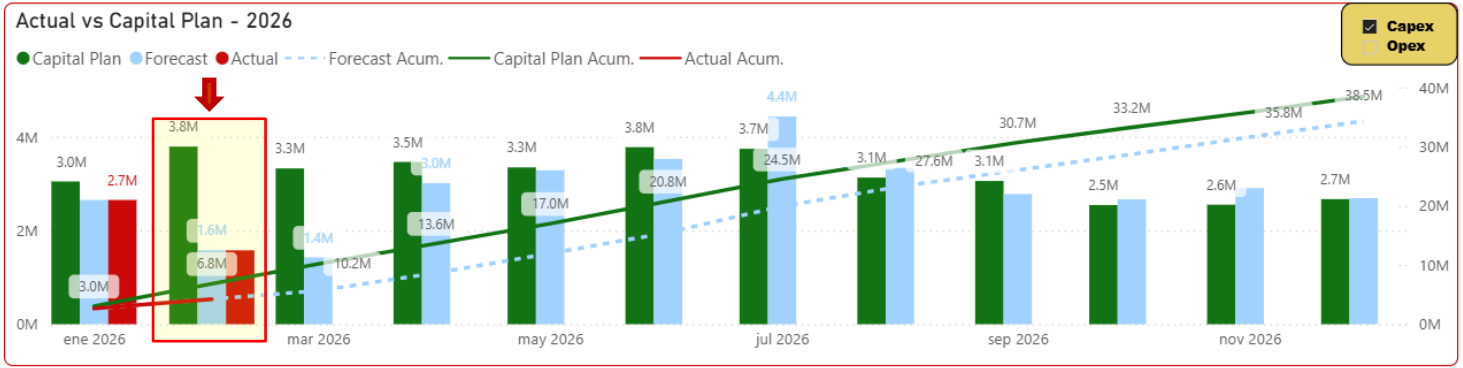

38.5M Capital Plan

34.3M Forecast

4.2M Actual to date

6.4M Open Commit

Summary by Projects to Feb-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Feb)	Act vs Prev. Fcst (Feb)
Plant Expansion 61 MTPY (FS)	Herman Aleman	0.89M	1.15M	1.15M	0.06M	0.56M
Pumps, thickeners&tanks optimization_FS	Herman Aleman	0.84M	0.13M	0.13M	-0.34M	0.08M
Grinding pumping system optimization	Herman Aleman	0.79M	0.00M	0.00M	-0.40M	0.00M
Crusher Relocation (FS)	Herman Aleman	0.71M	1.40M	1.40M	0.04M	0.36M
Pionero Waste Dump (FS)	Herman Aleman	0.49M	0.01M	0.01M	-0.15M	0.02M
Molybdenum Filter Replacement (FS)	Herman Aleman	0.42M	0.01M	0.01M	-0.28M	-0.05M
Total		**6.84M**	**4.23M**	**4.23M**	**-2.22M**	**1.38M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Plant Expansion 61 MTPY (FS)	5.82M	5.22M	1.15M	4.67M	0.40M	4.27M
Pumps, thickeners&tanks optimization_FS	5.03M	4.61M	0.13M	4.91M	0.01M	4.90M
Grinding pumping system optimization	4.75M	0.00M	0.00M	4.75M	0.81M	3.94M
Crusher Relocation (FS)	4.27M	4.47M	1.40M	2.88M	1.81M	1.07M
Moly Plant Optimization (FS)	3.00M	3.00M	0.02M	2.98M	0.28M	2.70M
Total	**38.45M**	**34.29M**	**4.23M**	**34.22M**	**103.77M**	

Goal for Mar-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Herman Aleman	Plant Expansion 61 MTPY (FS)	0.50M	0.07M
Herman Aleman	Pumps, thickeners&tanks optimization_FS	0.42M	0.04M
Herman Aleman	Grinding pumping system optimization	0.40M	0.00M
Herman Aleman	Crusher Relocation (FS)	0.36M	0.09M
Herman Aleman	Chalcobamba Feasibility	0.33M	0.01M
Herman Aleman	New 3 1/2 " grinding ball Hopper - mill (FS)	0.22M	0.02M
Herman Aleman	Additional Tailings Storage (FS)	0.15M	0.88M
Marcela Insignares	Chalcobamba Shift Turnover	0.13M	0.00M
Herman Aleman	Moly Plant Optimization (FS)	0.13M	0.02M
Herman Aleman	Thickeners Overflow Upgrade – Fifth pump FS	0.13M	0.00M
Total		**3.33M**	**1.43M**

Capex Portfolio Status / Implementation

CAPEX Report 2026 - Implementation (Feb-26)

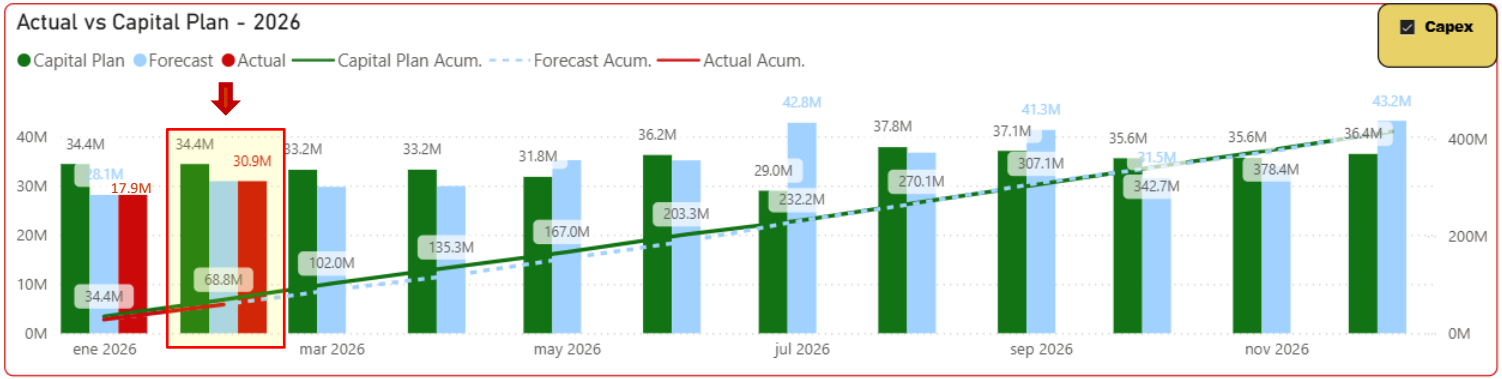

414.8M Capital Plan

418.5M Forecast

59.0M Actual to date

335.2M Open Commit

Summary by Projects to Feb-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Feb)	Act vs Prev. Fcst (Feb)
Pit FB Phase 6 - Infrastructure (IMP)	Reinaldo Ponce De León	10.09M	12.67M	12.67M	2.21M	6.91M
TD&RWI Pumping System (5&6)_Phase2 (IMP)	Alex Inostroza	8.44M	12.43M	12.43M	2.62M	6.72M
Tailings Dam Construction Stage VI (IMP)	Alex Inostroza	7.82M	7.21M	7.21M	-1.56M	2.39M
Chalcobamba 1 Sustaining	Reinaldo Ponce De León	6.60M	8.30M	8.30M	0.69M	4.01M
Pionero Waste Dump (IMP)	Reinaldo Ponce De León	6.42M	0.11M	0.11M	-3.18M	0.03M
Total		**68.79M**	**59.04M**	**59.04M**	**-3.48M**	**19.17M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Pit FB Phase 6 - Infrastructure (IMP)	48.42M	60.79M	12.67M	35.75M	45.43M	
Chalcobamba 1 Sustaining	42.43M	42.43M	8.30M	34.12M	74.65M	
Tailings Dam Construction Stage VI (IMP)	39.14M	39.00M	7.21M	31.94M	123.10M	
Pionero Waste Dump (IMP)	38.49M	38.49M	0.11M	38.38M	1.40M	36.98M
TSF 1 - Stg VII / VIII Facilities (IMP)	37.72M	32.05M	0.00M	37.72M	0.07M	37.65M
Total	**414.81M**	**418.51M**	**59.04M**	**355.76M**	**428.33M**	

Goal for Mar-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Alex Inostroza	TD&RWI Pumping System (5&6)_Phase2 (IMP)	4.37M	5.99M
Reinaldo Ponce De León	Pit FB Phase 6 - Infrastructure (IMP)	4.10M	5.57M
Reinaldo Ponce De León	Chalcobamba 1 Sustaining	3.38M	4.20M
Alex Inostroza	Column cells install. bulk flotat. (IMP)	3.31M	1.13M
Reinaldo Ponce De León	Pionero Waste Dump (IMP)	3.21M	0.35M
Alex Inostroza	Tailings Dam Construction Stage VI (IMP)	2.89M	3.91M
Reinaldo Ponce De León	Pit FB Phase 6B - Infrastructure (IMP)	2.30M	3.51M
Alex Inostroza	FB BWM-Se Control Short Term (IMP)	1.85M	1.44M
Total		**33.22M**	**29.75M**

Capex Portfolio Status / Land

CAPEX Report 2026 - Land (Feb-26)

Actual vs Capital Plan - 2026

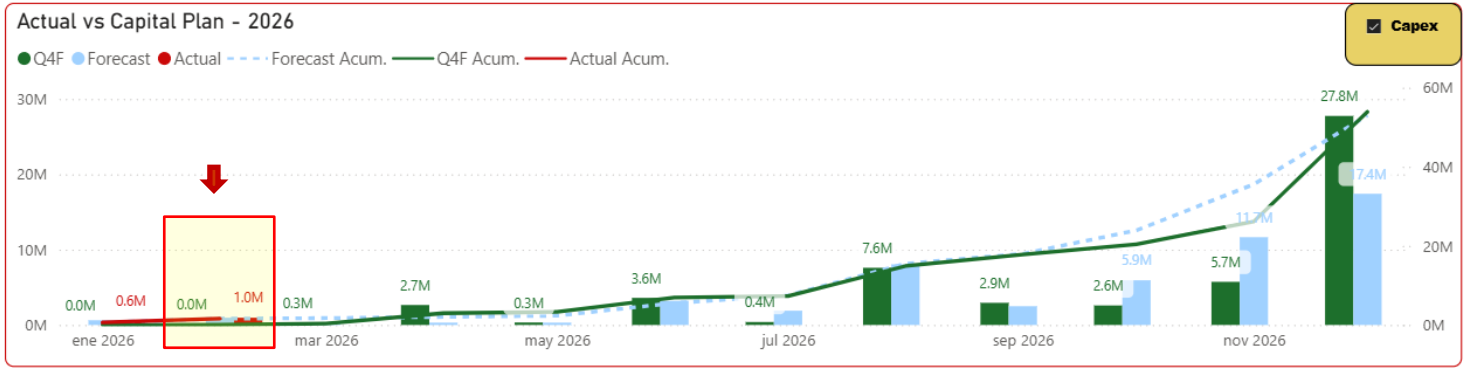

53.9M Capital Plan

53.0M Forecast

1.6M Actual to date

3.0M Open Commit

Summary by Projects to Feb-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Feb)	Act vs Prev. Fcst (Feb)
Social Liberation of Pumamarca(Sallahui)	Gonzalo Garcia	0.03M	0.46M	0.46M	0.03M	0.06M
"Triangulo" Land Purchase	Gonzalo Garcia	0.00M	0.00M	0.00M	0.00M	0.00M
Chalcobamba Land Access (Hancochiri)	Gonzalo Garcia	0.00M	0.00M	0.00M	0.00M	0.00M
FB Phase 7 Buffer Area Access	Gonzalo Garcia	0.00M	0.00M	0.00M	0.00M	0.00M
Huañaculla Land Access	Gonzalo Garcia	0.00M	0.10M	0.10M	0.10M	0.10M
Total		**0.03M**	**1.59M**	**1.59M**	**0.93M**	**-5.56M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
TSF2 Land Access (Communities)	11.45M	11.45M	0.00M	11.45M	0.00M	11.45M
TSF2 Land Access (Private Properties)	10.78M	10.78M	0.89M	9.89M	0.82M	9.07M
Chalcobamba Land Access (Hancochiri)	10.73M	0.00M	0.00M	10.73M	0.32M	10.41M
Stg3 - Sulfobamba Land Access	10.30M	10.30M	0.00M	10.30M	0.02M	10.29M
"Triangulo" Land Purchase	5.25M	5.25M	0.00M	5.25M	0.04M	5.21M
Total	**53.92M**	**53.01M**	**1.59M**	**52.33M**	**3.76M**	**48.58M**

Goal for Mar-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Gonzalo Garcia	Socorro buffer land access	0.30M	0.15M
Gonzalo Garcia	"Triangulo" Land Purchase	0.00M	0.00M
Gonzalo Garcia	Chalcobamba Land Access (Hancochiri)	0.00M	0.00M
Gonzalo Garcia	FB Phase 7 Buffer Area Access	0.00M	0.00M
Gonzalo Garcia	Huañaculla Land Access	0.00M	0.00M
Augusto Cavero	New access and checkpoint -North area	0.00M	0.00M
Gonzalo Garcia	Social Access to Socorro Land – Conveyor	0.00M	0.00M
Gonzalo Garcia	Social Liberation of Pumamarca(Sallahui)	0.00M	0.00M
Gonzalo Garcia	Stg3 - Sulfobamba Land Access	0.00M	0.00M
Gonzalo Garcia	TSF2 Land Access (Communities)	0.00M	0.00M
Gonzalo Garcia	TSF2 Land Access (Private Properties)	0.00M	0.00M
Total		**0.30M**	**0.15M**

Capex Portfolio Status / Resource Development

CAPEX Report 2026 - Resource Development (Feb-26)

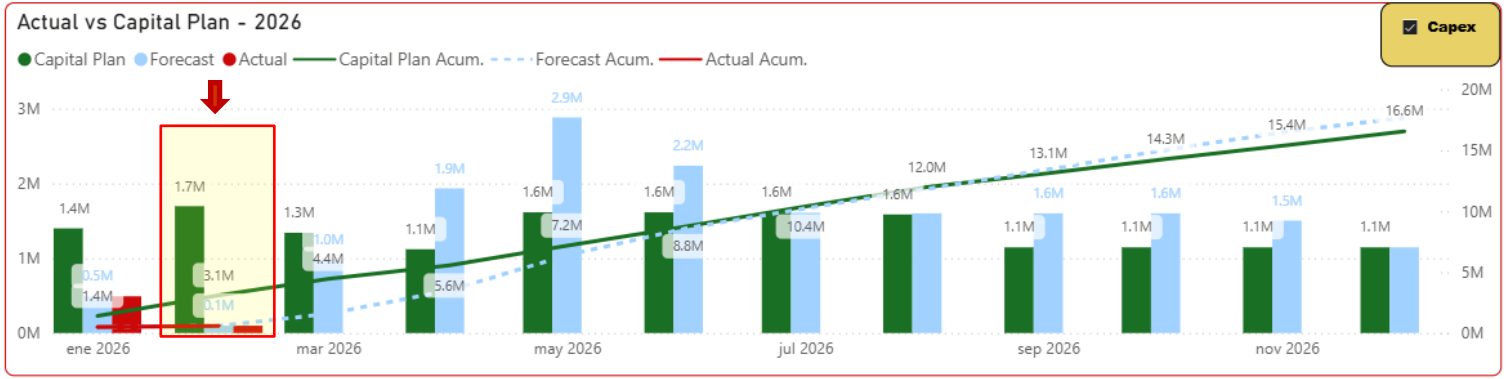

16.6M Capital Plan

17.2M Forecast

0.6M Actual to date

1.1M Open Commit

Summary by Projects to Feb-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Feb)	Act vs Prev. Fcst (Feb)
2025 CB SW Reserve Definition Drilling	Cesar Aguirre	1.34M	0.54M	0.54M	-0.58M	0.09M
2025-2026 FB Pit Reserve Def. Drilling	Cesar Aguirre	0.94M	-0.27M	-0.27M	-0.42M	0.05M
2021-22 CB Pit Reserve Definition Drilling	Cesar Aguirre	0.82M	-0.04M	-0.04M	-0.64M	-0.70M
2021-22 CB SW Reserve Definition Drilling	Cesar Aguirre	0.00M	0.01M	0.01M	0.01M	0.01M
2023-2024 FB Pit Reserve Def. Drilling	Cesar Aguirre	0.00M	0.00M	0.00M	0.00M	0.00M
Total		**3.10M**	**0.59M**	**0.59M**	**-1.60M**	**-1.62M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
2026-2027 CB Pit Reserve Definition Drilling	9.16M	9.16M	0.00M	9.16M	0.00M	9.16M
2025-2026 FB Pit Reserve Def. Drilling	3.72M	3.73M	-0.27M	3.99M	0.04M	3.95M
2025 CB SW Reserve Definition Drilling	2.66M	2.67M	0.54M	2.12M	0.27M	1.85M
2021-22 CB Pit Reserve Definition Drilling	1.02M	1.27M	-0.04M	1.06M	0.42M	0.64M
2021-22 CB SW Reserve Definition Drilling	0.00M	0.20M	0.01M	-0.01M	0.16M	
Total	**16.56M**	**17.68M**	**0.59M**	**15.97M**	**1.06M**	**14.91M**

Goal for Mar-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Cesar Aguirre	2025 CB SW Reserve Definition Drilling	0.67M	0.16M
Cesar Aguirre	2025-2026 FB Pit Reserve Def. Drilling	0.47M	0.46M
Cesar Aguirre	2021-22 CB Pit Reserve Definition Drilling	0.20M	0.26M
Cesar Aguirre	2021-22 CB SW Reserve Definition Drilling	0.00M	0.05M
Cesar Aguirre	2024-2025 FB Pit Reserve Def. Drilling	0.00M	0.06M
Total		**1.34M**	**0.98M**

Capex Portfolio Status / Maintenance

CAPEX Report 2026 - Maintenance (Feb-26)

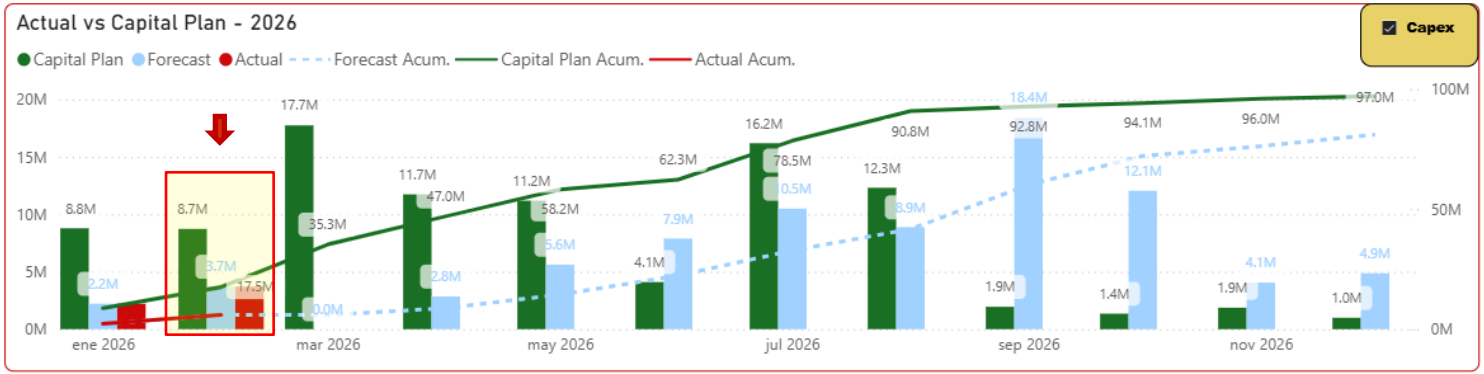

97.0M Capital Plan

81.1M Forecast

5.9M Actual to date

61.1M Open Commit

Summary by Projects to Feb-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Feb)	Act vs Prev. Fcst (Feb)
Ball Mill 02 Components Puchase	Hugo Albuqueque	4.00M	0.00M	0.00M	0.00M	0.00M
Overland Conveyor 4 Replacement 2025	Hugo Albuqueque	3.55M	3.02M	3.02M	-0.34M	1.44M
Truck KOM 930E Comp 2025-2027	Jimmy Ortiz	1.87M	1.12M	1.12M	-0.75M	1.12M
Drilling overhaul P&H 320XPC (TD003)	Jimmy Ortiz	1.63M	0.00M	0.00M	-1.03M	0.00M
Truck CAT 797F Comp 2025-2027	Jimmy Ortiz	1.50M	0.00M	0.00M	-1.50M	0.00M
Total		**17.52M**	**5.93M**	**5.93M**	**-5.03M**	**-4.17M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Truck KOM 930E Comp 2025-2027	16.49M	11.93M	1.12M	15.38M	2.61M	12.77M
Overland Conveyor 4 Replacement 2025	8.87M	4.66M	3.02M	5.85M	3.25M	2.60M
Truck CAT 797F Comp 2025-2027	7.28M	7.28M	0.00M	7.28M	16.94M	
Shovel P&P 4100 Comp 2025-2027	6.87M	6.87M	0.32M	6.55M	7.78M	
Shovel overhaul 2 P&H 41000 (SH003/S0004	6.48M	6.14M	-8.88E-16	6.48M	0.14M	6.35M
Total	**96.98M**	**81.07M**	**5.93M**	**91.06M**	**61.08M**	**29.98M**

Goal for Mar-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Jimmy Ortiz	Shovel CAT 6060 Comp 2025-2027	3.30M	0.00M
Jimmy Ortiz	Truck KOM 930E Comp 2025-2027	3.28M	0.00M
Hugo Albuqueque	Overland Conveyor 4 Replacement 2025	1.77M	0.00M
Jimmy Ortiz	Truck CAT 797F Comp 2025-2027	1.50M	0.00M
Jimmy Ortiz	Drill Electric Cat MD6640 Comp 2025-2027	1.32M	0.00M
Hugo Albuqueque	Shutdown Improvements 2026	0.87M	0.00M
Jimmy Ortiz	Auxiliary equipment for Maintenance Area	0.76M	0.00M
Jimmy Ortiz	Shovel overhaul 2 P&H 41000 (SH003/S0004	0.74M	0.00M
Jimmy Ortiz	Truck CAT 798 AC Comp 2025-2027	0.58M	0.00M
Jimmy Ortiz	Drilling overhaul P&H 320XPC (TD004)	0.55M	0.00M
Jimmy Ortiz	Excavator KOM PC2000 Comp 2025-2027	0.50M	0.00M
Jimmy Ortiz	Truck KOM 980E Comp 2025-2027	0.50M	0.00M
Total		**17.75M**	**0.00M**

Capex Portfolio Status / Technical Services

CAPEX Report 2026 - Technical Services (Feb-26)

Actual vs Capital Plan - 2026

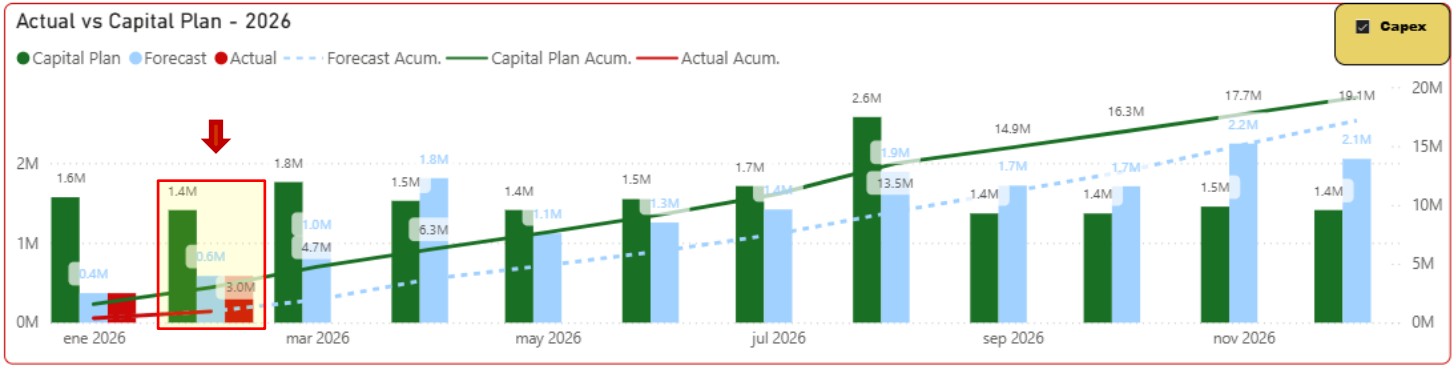

19.1M Capital Plan

17.2M Forecast

1.0M Actual to date

8.7M Open Commit

Summary by Projects to Feb-26

Name	P. Manager	Capital Plan	Act (YTD)	Act vs CP (Feb)	Act vs Prev. Fcst (Feb)
Dewatering Pit FB & CB 2025	Herminio Nieto	1.66M	0.35M	-0.54M	0.29M
Return of FB pit dewatering to East Chan	Herminio Nieto	0.60M	0.44M	0.02M	0.13M
2025-2026 Geotechnical Drilling FB	David Ojeda	0.53M	0.14M	-0.15M	0.14M
Dewatering Pit Program (FB, CB, etc)	Herminio Nieto	0.18M	0.00M	-0.18M	-0.18M
2022 Ferrobamba PIT & Waste Dam Geotech	David Ojeda	0.00M	0.00M	0.00M	-0.76M
Total		**2.98M**	**0.95M**	**-0.83M**	**-0.36M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Dewatering Pit Program (FB, CB, etc)	11.00M	0.00M	0.00M	11.00M	0.00M	11.00M
Dewatering Pit FB & CB 2025	4.53M	2.57M	0.35M	4.18M	2.57M	1.61M
Return of FB pit dewatering to East Chan	2.59M	2.59M	0.44M	2.15M	1.74M	0.41M
2025-2026 Geotechnical Drilling FB	1.00M	1.00M	0.14M	0.86M	0.38M	0.49M
2022 Ferrobamba PIT & Waste Dam Geotech	0.00M	0.00M	0.00M	0.00M	0.00M	0.00M
Total	**19.12M**	**17.16M**	**0.95M**	**18.17M**	**8.74M**	**9.43M**

Goal for Mar-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Herminio Nieto	Dewatering Pit Program (FB, CB, etc)	1.08M	0.00M
David Ojeda	2025-2026 Geotechnical Drilling FB	0.35M	0.11M
Herminio Nieto	Dewatering Pit FB & CB 2025	0.33M	0.33M
David Ojeda	2022 Ferrobamba PIT & Waste Dam Geotech	0.00M	0.00M
Herminio Nieto	Dewatering Pit FB & CB 2026	0.00M	0.30M
Herminio Nieto	Dewatering Pit Ferrobamba 2024	0.00M	0.00M
David Ojeda	FB Microseismic Control	0.00M	0.00M
David Ojeda	FB-CB Geotechnical Drilling 2025@2038	0.00M	0.00M
Herminio Nieto	Return of FB pit dewatering to East Chan	0.00M	0.25M
Total		**1.76M**	**0.99M**

Capex Portfolio Status / Others

CAPEX Report 2026 - Others (Feb-26)

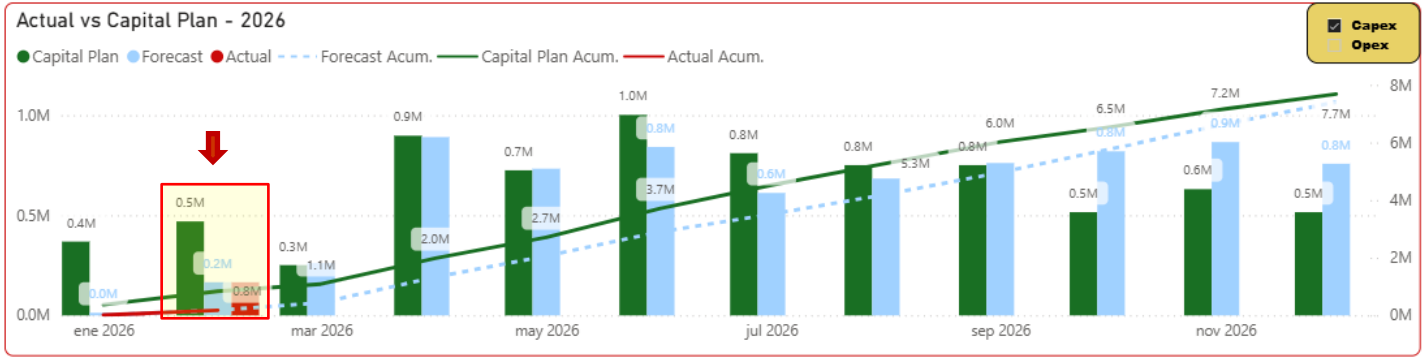

7.7M Capital Plan

7.4M Forecast

0.2M Actual to date

1.0M Open Commit

Summary by Projects to Feb-26

Name	P. Manager	Capital Plan	Forecast	Act (YTD)	Act vs CP (Feb)	Act vs Prev. Fcst (Feb)
Digital Operation Control Centre	Abdon Guillen	0.30M	0.00M	0.00M	-0.30M	0.00M
Process Water Improvement (FS)	Jean Vilchez	0.25M	0.05M	0.05M	-0.03M	0.04M
Paving of 13 Sections APU-CUZ road	Fernando Salinas	0.16M	0.00M	0.00M	-0.08M	-0.05M
FB BWM-FB & Huancarane (FS)	Jean Vilchez	0.13M	0.11M	0.11M	0.09M	-4.74M
Access to Haquira route	Marcos Cocas	0.00M	0.00M	0.00M	0.00M	0.00M
Total		**0.84M**	**0.18M**	**0.18M**	**-0.30M**	**-5.89M**

Total Year by Projects 2026

Name	Capital Plan	Forecast	Actual	Year To Go	Open Comm.	New Comm.
Huancuire Agreement (Phase 2)	3.64M	3.47M	0.00M	3.64M	0.00M	3.64M
Paving of 13 Sections APU-CUZ road	1.30M	1.13M	0.00M	1.30M	0.00M	1.30M
Selenium treatment plant (FS)	0.94M	0.94M	0.00M	0.94M	0.00M	0.94M
Process Water Improvement (FS)	0.51M	0.51M	0.05M	0.46M	0.04M	0.42M
Camps for Public Safety - HHR Wincho&Con	0.46M	0.00M	0.00M	0.46M	0.42M	0.03M
Total	**7.69M**	**7.40M**	**0.18M**	**7.51M**	**1.02M**	**6.49M**

Goal for Mar-26

P. Manager / Std. Lead	Name	Capital Plan	Forecast
Fernando Salinas	Paving of 13 Sections APU-CUZ road	0.08M	0.08M
Jean Vilchez	Process Water Improvement (FS)	0.06M	0.04M
Jean Vilchez	FB BWM-FB & Huancarane (FS)	0.06M	0.13M
Henry Delgado	LB Centralization of fire alarms	0.05M	0.00M
Marcos Cocas	Access to Haquira route	0.00M	0.00M
Marcos Cocas	Access to Inquilpata route	0.00M	0.00M
Augusto Cavero	Camps for Public Safety - HHR Wincho&Con	0.00M	0.00M
Abdon Guillen	Digital Operation Control Centre	0.00M	0.00M
Jean Vilchez	Ferrobamba Basin Water Management (FS)	0.00M	0.01M
Fernando Salinas	Heavy Haul Road 02 Bridges Reinforcement	0.00M	0.00M
Maria Millones	Huancuire Agreement	0.00M	0.00M
Total		**0.25M**	**0.26M**

Opex Development

Opex Portfolio Status

OPEX Report 2026 (As of Feb-26)

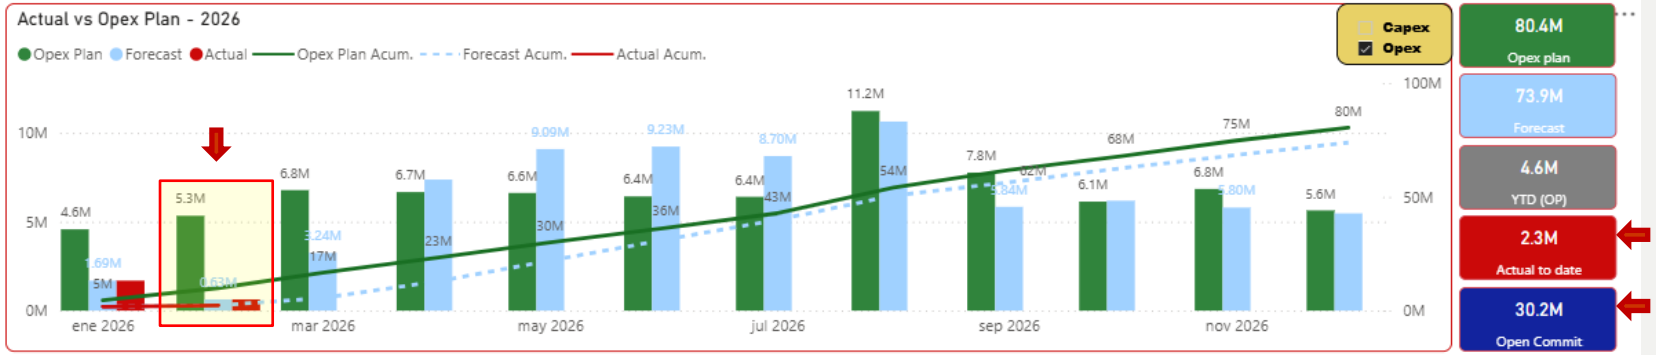

Summary by Areas (YTD)







Summary by Areas with Year To Go 2026

Grupo	Opex Plan	Forecast	Actual	YTG (OP)	O. Comm.	New Comm.
Logistic	12.65M	12.79M	0.88M	11.77M	4.52M	7.25M
Others	0.94M	0.93M	0.02M	0.92M	0.78M	0.14M
Permits	7.02M	6.82M	0.06M	6.96M	5.16M	1.80M
Resource Development	0.00M	0.00M	0.00M	0.00M	0.54M	
Studies	59.79M	53.33M	1.35M	58.44M	19.15M	39.28M
Total	**80.41M**	**73.86M**	**2.32M**	**78.09M**	**30.17M**	**47.93M**

Status for Feb-26

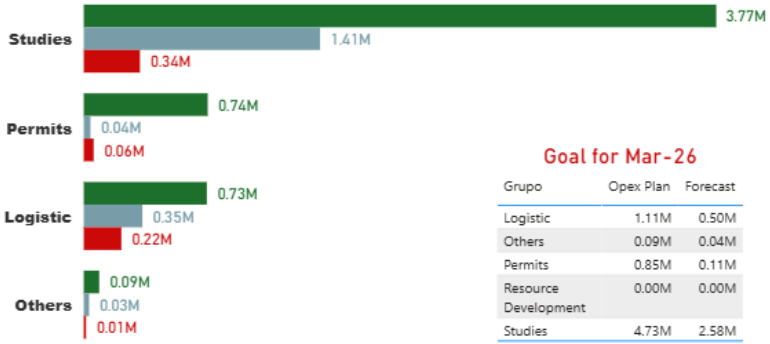

* Previous forecast

Goal for Mar-26

Grupo	Opex Plan	Forecast
Logistic	1.11M	0.50M
Others	0.09M	0.04M
Permits	0.85M	0.11M
Resource Development	0.00M	0.00M
Studies	4.73M	2.58M
Total	**6.78M**	**3.24M**

Opex Portfolio Status / Studies

OPEX Report 2026 - Studies (Feb-26)

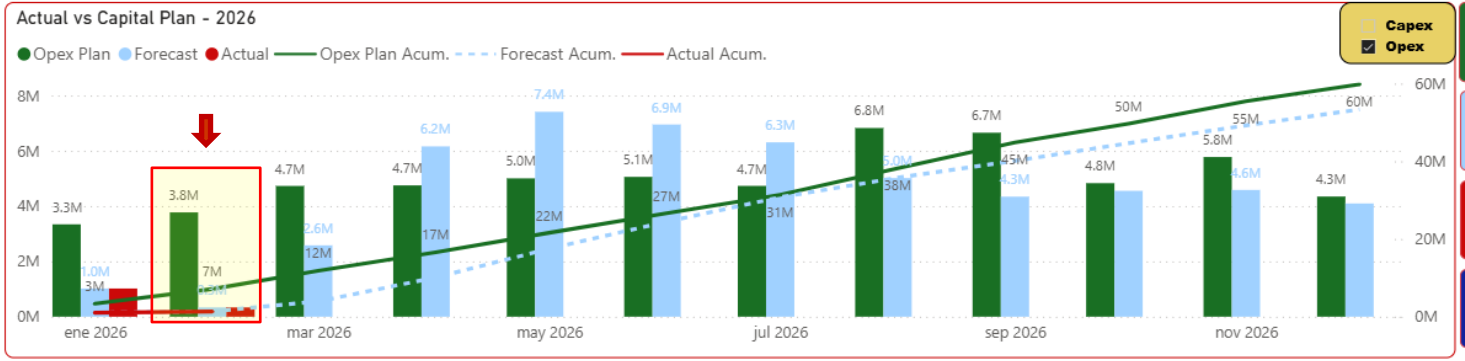

59.8M Opex plan

53.3M Forecast

1.4M Actual to date

19.2M Open Commit

Summary by Projects (YTD)

Name	Opex Plan	Forecast	Act to date	Act vs OP (Feb)	Act vs Prev. Fcst (Feb)
Ampliacion Planta 81 MTPY	2.62M			-1.31M	
Tailings Storage Facility 2 PFS	2.30M	0.84M	0.84M	-1.39M	-1.00M
Selenium treatment plant (PFS)	0.94M	0.15M	0.15M	-0.31M	0.07M
FB Underground (SC)	0.55M	0.11M	0.11M	-0.09M	-0.03M
Material Movement/Hybrid trucks(PFS)	0.23M	0.00M	0.00M	-0.21M	0.00M
Total	**7.11M**	**1.35M**	**1.35M**	**-3.44M**	**-1.07M**

Summary by Projects with Year To Go 2026

Name	Opex Plan	Forecast	Actual	YTG	O.Comm.	New Comm.
Tailings Storage Facility 2 PFS	21.20M	17.71M	0.84M	20.35M	13.93M	6.42M
Ampliacion Planta 81 MTPY	15.61M			15.61M	1.24M	14.37M
FB Underground (SC)	7.41M	3.37M	0.11M	7.30M	0.25M	7.05M
Reposicion Chalcobamba (SC)	5.14M	17.30M	0.00M	5.14M	0.00M	5.14M
Material Movement/Hybrid trucks(PFS)	4.68M	1.54M	0.00M	4.68M	1.58M	3.11M
Sulfobamba PFS	2.83M	2.66M	0.14M	2.69M	0.66M	2.02M
Total	**59.79M**	**53.33M**	**1.35M**	**58.44M**	**19.15M**	**39.28M**

Goal for Mar-26

Project Manager / Study Lead	Name	Opex Plan	Forecast
Yessenia Granados	Tailings Storage Facility 2 PFS	2.12M	1.81M
Herman Aleman	Ampliacion Planta 81 MTPY	1.28M	
Marcela Insignares	Material Movement/Hybrid trucks(PFS)	0.56M	0.00M
Marcos Cocas	FB Underground (SC)	0.27M	0.07M
Jean Vilchez	Selenium treatment plant (PFS)	0.15M	0.11M
Marcos Cocas	Reposicion Chalcobamba (SC)	0.13M	0.39M
Marcos Cocas	Sulfobamba PFS	0.10M	
Yessenia Granados	Additional Tailings Storage PFS	0.08M	0.08M
Total		**4.73M**	**2.58M**

Opex Portfolio Status / Logistic

OPEX Report 2026 - Logistic (Feb-26)

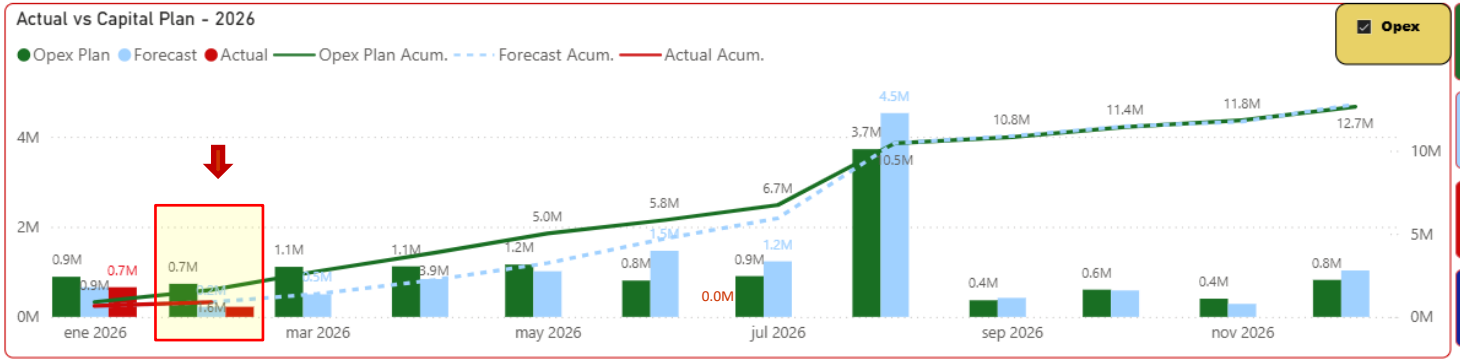

12.7M Opex plan

12.1M Forecast

0.7M Actual to date

4.5M Open Commit

Summary by Projects (YTD)

Name	Opex Plan	Forecast	Act to date	Act vs OP (Feb)	Act vs Prev. Fcst (Feb)
Ing. Vias nacionales(Cusco-Apurimac)	1.18M	0.74M	0.74M	-0.35M	-0.09M
Logistic Options PFS - Roads (Monitoreos 2020 / Ing 2021)	0.23M	0.14M	0.14M	-0.05M	-0.04M
LB-Exit Routes	0.20M	0.00M	0.00M	-0.10M	0.00M
Route LB-Haquira-Izcahuaca-Marcona	0.02M	0.00M	0.00M	-0.01M	0.00M
Heavy Haul Road	0.00M	0.00M	0.00M	0.00M	0.00M
Total	**1.62M**	**0.88M**	**0.88M**	**-0.51M**	**-0.13M**

Summary by Projects with Year To Go 2026

Name	Opex Plan	Forecast	Actual	YTG	O.Comm.	New Comm.
Ing. Vias nacionales(Cusco-Apurimac)	4.76M	4.76M	0.74M	4.02M	4.47M	
Route LB-Haquira-Izcahuaca-Marcona	3.32M	3.32M	0.00M	3.32M	0.00M	3.32M
Logistic Options PFS - Roads (Monitoreos 2020 / Ing 2021)	2.34M	2.47M	0.14M	2.20M	0.05M	2.15M
LB-Exit Routes	1.21M	1.21M	0.00M	1.21M	0.00M	1.21M
Logistic Options PFS - Pipeline	0.53M	0.53M	0.00M	0.53M	0.00M	0.53M
Total	**12.65M**	**12.79M**	**0.88M**	**11.77M**	**4.52M**	**7.25M**

Goal for Mar-26

Project Manager / Study Lead	Name	Opex Plan	Forecast
Robert Villanueva	Ing. Vias nacionales(Cusco-Apurimac)	0.73M	0.36M
Marcos Cocas	Logistic Options PFS - Pipeline	0.11M	0.00M
Marcos Cocas	LB-Exit Routes	0.10M	0.00M
Marcos Cocas	Logistic Options PFS - Roads (Monitoreos 2020 / Ing 2021)	0.10M	0.14M
Marcos Cocas	Train LB-Marcona	0.06M	0.00M
Marcos Cocas	Route LB-Haquira-Izcahuaca-Marcona	0.01M	0.00M
Total		**1.11M**	**0.50M**
