2026 APFs Plan/ Minor and Medium Projects

Abril 14th 2026

ICMM International Council on Mining & Metals | MINING WITH PRINCIPLES

2026 Medium & Minor Projects APFs Submission

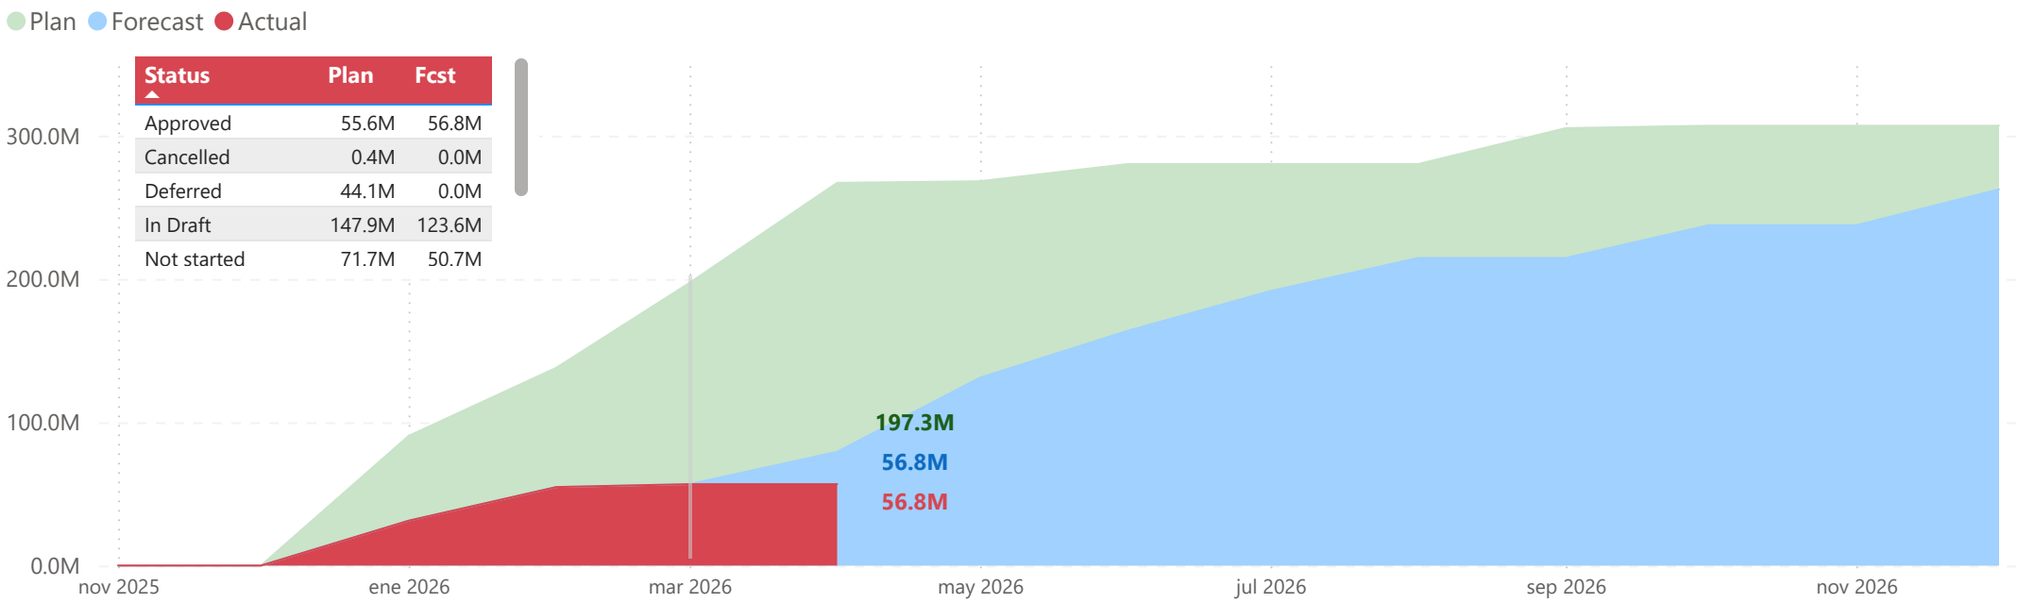

Status	Plan	Fcst
Approved	55.6M	56.8M
Cancelled	0.4M	0.0M
Deferred	44.1M	0.0M
In Draft	147.9M	123.6M
Not started	71.7M	50.7M

306.9M
Original Plan

262.5M
Forecast

56.8M
Submitted

56.8M
Approved

350.0K
Cancelled

2026 APF Approval Status

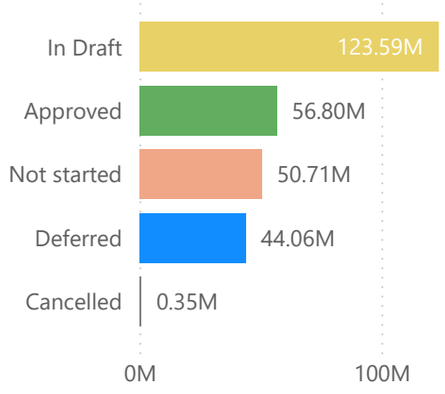

Upcoming APFs (Until Abr-26)

Code	Name	Phase	Responsible	Status	Re sched.	Plan	Fcst	.	Fcst Date
5200P-015412	Power System (IMP)	IMP	Herman Aleman	In Draft	1	8.0M	8.0M		30/04/2026
5200P-017549	Dispersant Reagent Preparat. Plant (IMP)	IMP	Herman Aleman	In Draft	1	5.3M	5.3M		30/04/2026
5200P-017656	Civil Plant Infrastucture (Mechanical)	IMP	Hugo Alburqueque	In Draft	1	3.5M	3.5M		27/04/2026
5200P-016545	Chalcobamba Mobile Fuel Station (IMP)	IMP	Eduardo Guanilo	In Draft	1	2.3M	2.3M		30/04/2026
5200P-017657	Civil Plant Infrastucture (E&I)	IMP	Hugo Alburqueque	In Draft	1	2.1M	2.1M		27/04/2026
5200P-016556	Chalcobamba Shift Turnover (IMP)	FS	Eduardo Guanilo	In Draft	1	1.4M	1.4M		30/04/2026
Total						**22.6M**	**22.6M**		

Re scheduled APFs

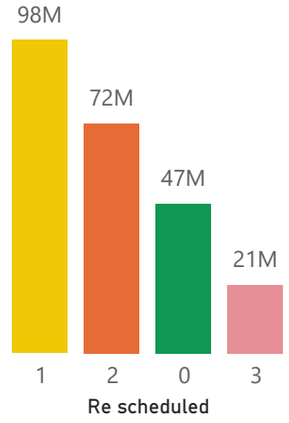

2026 Medium & Minor Projects APFs Submission

RoutingFcast

03/01/2026

31/05/2026

Medium & Minor APF's until Mar-26

Code	Name	In Plan / Out of Plan	Responsible	Status	Plan	Fcst	RoutingPlan	Fcst Date	Delay Fcast vs Plan	Re scheduled
5200P-017702	TD-004 (P&H 320) Drill Rig Replacement	Out of Plan	Eduardo Guanilo	Approved	0.0M	8.7M	03/01/2026	3/01/2026	0	1
5200P-015753	TD&RWI Reclaim Water Chuspiri (IMP)	In Plan	Alex Inostroza	Approved	12.1M	12.1M	05/01/2026	5/01/2026	0	0
5200P-017133	DMO Ferro 2 (IMP)	In Plan	Herman Aleman	Approved	10.6M	10.5M	03/01/2026	12/01/2026	9	1
5200P-016558	Dynamic Reactive Compensation (FS)	In Plan	Herman Aleman	Cancelled	0.4M	0.0M	23/01/2026	23/01/2026	0	1
5200P-017712	Dewatering Pit FB & CB 2026	In Plan	Herminio Nieto	Approved	11.0M	11.0M	04/02/2026	17/02/2026	13	2
5200P-017640	New light EQ maintenance workshop (IMP)	In Plan	Marcela Insignares	Approved	4.7M	3.3M	30/01/2026	17/02/2026	18	1
5200P-017153	2026-2027 CB Pit Reserve Definition Dril	In Plan	Cesar Aguirre	Approved	15.2M	9.2M	12/01/2026	22/02/2026	41	3
5200P-017737	Chalcobamba Geotechnical Drilling 2026	Out of Plan	David Ojeda	Approved	2.0M	2.0M	30/03/2026	17/03/2026	-13	1
5200P-017657	Civil Plant Infrastucture (E&I)	In Plan	Hugo Alburqueque	In Draft	2.1M	2.1M	30/01/2026	27/04/2026	87	1
5200P-017656	Civil Plant Infrastucture (Mechanical)	In Plan	Hugo Alburqueque	In Draft	3.5M	3.5M	13/02/2026	27/04/2026	73	1
5200P-016545	Chalcobamba Mobile Fuel Station (IMP)	In Plan	Eduardo Guanilo	In Draft	2.3M	2.3M	30/04/2026	30/04/2026	0	1
5200P-016556	Chalcobamba Shift Turnover (IMP)	In Plan	Eduardo Guanilo	In Draft	1.4M	1.4M	30/04/2026	30/04/2026	0	1
5200P-017549	Dispersant Reagent Preparat. Plant (IMP)	In Plan	Herman Aleman	In Draft	5.3M	5.3M	23/01/2026	30/04/2026	97	1
5200P-015412	Power System (IMP)	In Plan	Herman Aleman	In Draft	8.0M	8.0M	01/03/2026	30/04/2026	60	1
5200P-017232	New 3½" grinding ball hopper - mill (IMP)	In Plan	Herman Aleman	In Draft	2.4M	2.4M	23/01/2026	4/05/2026	101	1
5200P-015896	Camp XP Potable Water Plant Adaptation (IMP)	In Plan	Herman Aleman	Under review-DEV	1.3M	1.3M	20/01/2026	10/05/2026	110	2
5200P-017081	Chutes system optimization_Pebbles Area	In Plan	Herman Aleman	In Draft	1.1M	1.1M	28/01/2026	10/05/2026	102	2
5200P-017054	Pumps, thickeners&tanks optimization (IMP)	In Plan	Herman Aleman	In Draft	6.6M	6.6M	15/03/2026	10/05/2026	56	3
5200P-017673	02 Modular Tanks at the Huancarane Fuel Station	In Plan	Marcela Insignares	In Draft	1.7M	1.7M	04/10/2026	15/05/2026	-142	2
5200P-017654	Appron Feeder 2 Overhaul	In Plan	Hugo Alburqueque	In Draft	1.3M	1.3M	30/01/2026	15/05/2026	105	2
5200P-014972	Auxiliary equipment for Maintenance Area	In Plan	Jimmy Ortiz	In Draft	0.8M	0.8M	15/01/2026	15/05/2026	120	3
5200P-015578	Drilling overhaul CAT MD6640 (TD007)	In Plan	Jimmy Ortiz	In Draft	4.8M	4.8M	31/01/2026	15/05/2026	104	3
5200P-014966	FB Auxiliary equipment for drainage	In Plan	Eduardo Guanilo	Not started	2.2M	2.2M	30/04/2026	15/05/2026	15	1
5200P-014854	IT Projects 2022@2040	In Plan	Hermes Guevara	Not started	27.2M	6.2M	15/04/2026	15/05/2026	30	2
5200P-014914	Overland Conveyor 3 Replacement LoA	In Plan	Hugo Alburqueque	In Draft	33.0M	8.7M	27/02/2026	15/05/2026	77	2
5200P-017533	Primary Crushing–Apron Feeders Overhaul	In Plan	Hugo Alburqueque	Not started	1.3M	1.3M	16/01/2026	15/05/2026	119	2
5200P-017631	Shutdown Improvements 2026	In Plan	Hugo Alburqueque	In Draft	1.7M	1.7M	23/01/2026	15/05/2026	112	2
5200P-017176	Storm Detection System Upgrade	In Plan	Hermes Guevara	Not started	1.1M	1.1M	15/05/2026	15/05/2026	0	1
5200P-017548	Process Water Improvement (IMP)	In Plan	Alex Inostroza	In Draft	9.5M	9.5M	31/03/2026	30/05/2026	60	1
5200P-016533	Selenium treatment plant (FS)	In Plan	Jean Vilchez	In Draft	0.9M	0.9M	30/01/2026	30/05/2026	120	2
Total					**175.5M**	**131.1M**				

2026 Medium & Minor Projects APFs Submission

RoutingFca...

01/06/2026

31/12/2026

Medium & Minor APF's from Apr-26 to Dec-26

Code	Name	In Plan / Out of Plan	Responsible	Status	Plan	Fcst	RoutingPlan	Fcst Date	Delay Fcast vs Plan	Re scheduled
5200P-017547	Molybdenum Filter Replacement (IMP)	In Plan	Herman Aleman	Not started	3.1M	3.1M	23/01/2026	10/06/2026	138	2
5200P-017223	Grinding Expert System Renewal	In Plan	Hermes Guevara	Not started	1.4M	1.4M	15/06/2026	15/06/2026	0	0
5200P-016323	FB BWM-Sediment pond Jalansiricocha(IMP)	In Plan	Alex Inostroza	Under review-DEV	5.0M	5.0M	30/01/2026	20/06/2026	141	2
5200P-015433	Bulk Flotation System Control Optim.	In Plan	Hermes Guevara	Not started	8.9M	8.9M	30/06/2026	30/06/2026	0	1
5200P-015817	CRG001 Components Purchase	In Plan	Hugo Alburqueque	In Draft	1.8M	1.8M	30/01/2026	30/06/2026	151	1
5200P-016563	Fuel consumption optimization	In Plan	Hermes Guevara	Not started	1.7M	1.7M	30/06/2026	30/06/2026	0	1
5200P-015397	Site Invasion Material Risk Reduction P3	In Plan	Reinaldo Ponce De León	In Draft	10.8M	10.8M	31/03/2026	30/06/2026	91	0
5200P-017648	XP Camp Recovery & Expansion Ph1 (IMP)	In Plan	Marcela Insignares	In Draft	11.2M	11.2M	07/04/2026	10/07/2026	94	2
5200P-017562	Gets Drop Detection System Replacement	In Plan	Eduardo Guanilo	Not started	2.5M	2.5M	15/04/2026	30/07/2026	106	2
5200P-017152	Thickeners Overflow Upgrade 5th pump (IMP)	In Plan	Herman Aleman	In Draft	14.1M	14.1M	09/01/2026	30/07/2026	202	2
5200P-017222	Moly Plant Optimization (IMP)	In Plan	Herman Aleman	In Draft	23.1M	23.1M	15/04/2026	30/08/2026	137	1
5200P-014454	“Triangulo” Land Purchase	In Plan	Gonzalo Garcia	Not started	22.3M	22.3M	02/03/2026	11/10/2026	223	0
5200P-017192	4th Copper Filter Installation (FS)	In Plan	Herman Aleman	In Draft	0.5M	0.5M	02/01/2026	30/10/2026	301	2
5200P-017544	Plant Expansion 81 MTPY (FS)	In Plan	Herman Aleman	Under review-BE	25.1M	25.1M	21/09/2026	15/12/2026	85	1
Total					**131.4M**	**131.4M**				
